

EXHIBIT

A



THE RUINS MIXED-USE DEVELOPMENT

Watertown, SD

Prepared for Red River State Bank
May 24, 2024

CONSTRUCTION OBSERVATION REPORT



May 24th, 2024

Charles Aarestad
Executive Vice President
Red River State Bank
300 2nd Ave West
Halstad, MN 56548

Re: The Ruins Mixed-use Development
Watertown, SD

Project No. 24-020

Dear Mr. Aarestad:

Gehrtz Construction Services (GCS) is pleased to present our independent third-party inspection and report for The Ruins. We understand the subject is an under construction 63-unit mid/high rise property at 315 East Kemp Ave in Watertown, SD. Upon completion, the property will consist of a single, four-story apartment building with on-grade parking and first floor retail/ commercial space occupied by the City of Watertown.

A full and detailed inspection has been created documenting observations made on site April 17th, 2024. GCS personnel arrived on site around 8:00 AM and completed the building inspection by around 3:30 PM. The weather at the beginning of the site inspection was cloudy, windy (22 MPH, Gusting to 30 MPH) and approximately 45 degrees F. Rain and wind had been present in the 12 hours leading up to the site inspection. At the conclusion of the inspection, the weather was sunny, windy (17 MPH, Gusting to 24 MPH) and approximately 55-degree F.

The accounts documented in this report represent the opinion of GCS as the percentage complete of each subcontract. The report is structured to match the sworn construction statement provided by Red River State Bank as a reference for the subcontractors and work packages outstanding. Assumptions made regarding the scope of work for each of the subcontractor packages have been documented throughout the report. Building plans or permit plans were not available at the time of the inspection. The floor plans that were provided did not match the final layout of the building.

Thank you for the opportunity, please do not hesitate to reach out with any questions.

Sincerely,

A handwritten signature in black ink, appearing to read "Matt Gehrtz", with a long horizontal line extending to the right.

Matt Gehrtz
Principal Construction Manager

CONTENTS

Contents	2
Concrete Waterproofing & Insulation	3
Gypcrete	3
CMU Block	4
Misc. Metals	5
General W&L Rough Carpentry Labor	6
General W&L Finish Carpentry Labor	7
Millwork - Cabinets	8
Countertops – Kitchen & Bathroom	9
Bathroom Vanities	10
Moisture Protection	11
Masonry	12
Metal Siding/Metal Panels	13
Commercial Doors/Frames/Hardware	14
Vinyl Windows (Supply Only)	14
Glass & Glazing	14
Drywall	15
Carpet	16
Painting/Staining	17
Fill nail holes	18
Postal Specialties/Bike rack/Door markers	18
Fire Extinguishers & Cabinets	19
Ceiling Fans	20
Closet Shelving	21
Toilets and Accessories	22
Appliances & AC Units	23
Kitchen Sinks/Faucets	24
Bath Faucets/Shower Heads	25
Bathroom Mirrors	26
Window Treatments	27
Conveying Systems	27
Building Sprinkler	28
Plumbing	29
HVAC	30
Electrical/Security System	31
Paving and Sidewalks	32
Bid Packages Not Applicable for this Site Inspection	33
Additional Considerations	34
Appendix 1 – Unit Speicific Punch Lists	35

CONCRETE WATERPROOFING & INSULATION

Approximate Progress: 80% Complete

- No observed spray foam or seal at all AC sleeve penetrations.
- No observed foam seal at any exterior louvers

Potential Deficiencies:

- Overspray of spray foam observed at the transition from the brick stair to the metal siding at various locations.



Missing Insulation at AC Sleeve



Spray Foam Overspray



Exterior Louver

GYPCRETE

Approximate Progress: 99% Complete

- Observed all gypcrete completed at floors 3 and 4.
- In our opinion, the remaining work for this bid package is minor and/or punch list related items.

Potential Deficiencies:

- Bubbles and/or shale/debris observed at the surface of the floor in several areas, resulting in a potential concern with flooring installation.



Observed Gypcrete bubbling in Numerous locations.



Observed hole in floor in 3rd Floor Unit, Living Room.

CMU BLOCK

****Scope of Work**** Our assumption is this work package performed the work associated with the installation of spray-applied weather barrier on the 1st floor CMU block up to and including the precast plank on 2nd floor.

Approximate Progress: 75% Complete

- The exterior work appeared to be complete at the time of the inspection.
- In our opinion, it appears that there is still work to be completed in the common/community shared space on 1st floor. The extent of the scope of the work was not able to be determined without a permit set of plans. The current floor plan does not match the construction documents observed on site.

Potential Deficiencies:

- The spray-applied weather barrier at the edges of the precast planks at 2nd floor was not properly completed. As a result, significant moisture penetration along the CMU walls was observed at the time of the inspection.
- None of the CMU control joints were caulked or sealed prior to the spray-applied weather barrier.
- In our opinion, there is concern with the transition of the Tyvek weather barrier to the CMU block at the stair towers.



Moisture Observed on North wall, 1st Floor.



Moisture Observed on North wall, 1st Floor.



Moisture Observed on North wall, 1st Floor.



Tyvek to Spray Applied Transition



Precast Plank Ends Exposed

MISC. METALS

Approximate Progress: 80% Complete

- o Exterior: Bollards to be supplied and/or set.
- o 1st Floor: Roof Access ladder appeared to be located and stored on the first floor.
- o 2nd Floor: Missing Railing in West Stairwell
- o 4th Floor: Roof access ladder installation incomplete.

Potential Deficiencies: None observed.



4th Floor Roof Access Ladder
not Installed.



Access Ladder stored on site,
1st Floor.



Handrail Missing, West Stair
Tower

GENERAL W&L ROUGH CARPENTRY LABOR

****Scope of Work**** Our assumption is this work package performed the work associated with the installation of the Tyvek building wrap and residential windows 2nd-4th floors.

Approximate Progress: 75% Complete

- o Window installation approximately 90% completed. Missing windows on the south elevation of the building. One window missing on the north side of the east elevation, 2nd floor.
- o Building wrap installed on all elevations of the building.

Potential Deficiencies:


- o Observed various hold down plates not tight to underside of precast.
- o In our opinion, the Tyvek Building Wrap has deteriorated from the time of installation to the time of the inspection. Manufacturer inspection required to determine if current Tyvek building wrap is acceptable for warranty.
- o 3M Flashing Tape used to flash in the jambs and head of the windows. In our opinion, this may be a concern for the warrantability of the building wrap on the entire building since it is not a Tyvek product.
- o Transition from building wrap to masonry block was not terminated properly and could be the source for water penetration in the future.
- o Observed approx. 45-50 windows with moisture penetration on the north and east elevations of the building.
- o Observed approx. 10-15 windows with either broken or missing glass.
- o Observed approx. 12-17 windows with broken or malfunctioning latches and/or cranks.
- o Observed approx. 6-10 window frames that appeared to be warped or not leveled, causing operation



Loose Hold down Plate



Broken Window Pane



Broken Window Pane



Observed Water Damage



Faded Tyvek, 3M Tape on Windows

GENERAL W&L FINISH CARPENTRY LABOR

Approximate Progress: 75% Complete


- Exterior/Stairs: 50% Complete
 - Missing door frames in all stair towers.
 - Frames, doors, and hardware need to be installed.
 - Top Cap on 4th floor stair wall missing.
- 1st Floor: 0% Complete
- 2nd Floor: 90% Complete
 - The corridor wood base has yet to be installed.
 - Spring hinges on all unit entry doors need to be adjusted.
- 3rd Floor: 85% Complete
 - The corridor wood base has yet to be installed.
 - Spring hinges on all unit entry doors need to be adjusted.
 - Missing Door Hardware on a few interior doors throughout the floor
- 4th Floor: 90% Complete
 - The corridor wood base has yet to be installed.
 - Spring hinges on all unit entry doors need to be adjusted.

Potential Deficiencies:


- Observed several damaged unit entry doors.
- Observed numerous units which had the back of the closet bi-fold doors ripped down to fit the opening.
- Observed wood base installed prior to unit flooring and no gap between the subsurface and the bottom of the base.
- Observed no trim/casing around the AC cans. We are unsure how this finish condition should be, but it is an area of potential additional work required.



Back side of Bi-Fold Doors
Ripped Down to fit opening.



Stair Frame, Door, and
Hardware to be completed.



Hallway Base Missing,
2nd Floor.

MILLWORK - CABINETS

Approximate Progress: 85% Complete


- 2nd Floor: 90% Complete
 - Observed 1 unit where cabinet installation was incomplete.
- 3rd Floor: 75% Complete
 - Observed 17 units with at least one missing upper cabinet.
 - Observed 4 units with all upper and base cabinets installed.
- 4th Floor: 95% Complete
 - Observed all cabinets to be in place. Only punch list related items to be completed.

Potential Deficiencies:


- Observed locations where cabinet installation did not match countertops or necessary clearance for appliances to fit.




Install all Cabinets, 2nd Floor

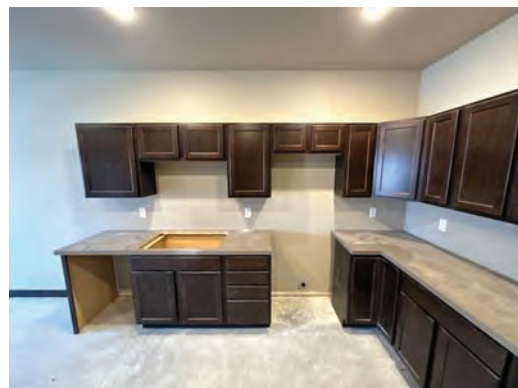

2nd Floor Unit

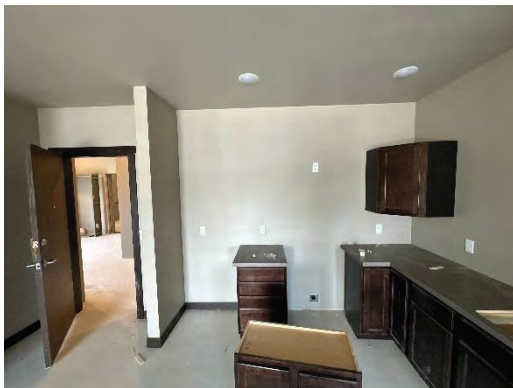

Missing Upper Cabinet, 3rd Floor

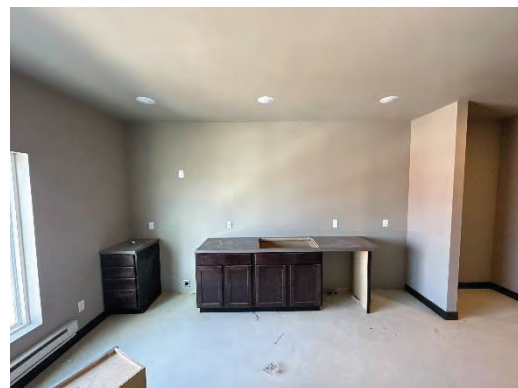

Missing Upper Cabinet, 3rd Floor



4th Floor Unit



4th Floor Unit


COUNTERTOPS – KITCHEN & BATHROOM

Approximate Progress: 90% Complete

- 2nd Floor: 85% Complete
 - Observed 2 units where countertop installation was incomplete.
- 3rd Floor: 95% Complete
 - Observed all countertops to be in place. Only punch list related items to be completed.
- 4th Floor: 90% Complete
 - Observed 1 unit where countertop installation was incomplete.
 - Observed 20 units where countertops were in place. Only punch list related items to be completed.

Potential Deficiencies:


- Observed numerous locations where the overhangs of the countertops were inconsistent. In some cases, overhang of the countertops will prevent installation of the range.

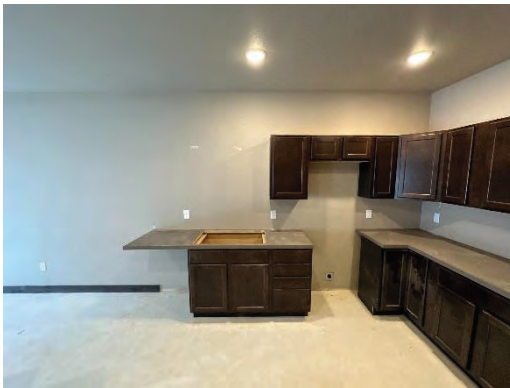

3rd Floor Unit, Adjustment Required



2nd Floor Unit, Missing Top

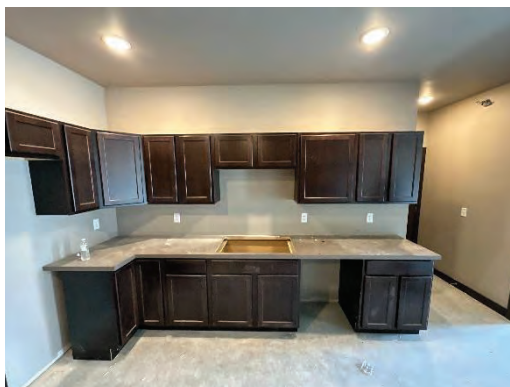


2nd Floor Unit, Typical Condition

BATHROOM VANITIES

Approximate Progress: 90% Complete


- 2nd Floor: 90% Complete
 - Observed 2 Units where vanity was not installed.
- 3rd Floor: 90% Complete
 - Observed 2 Units where vanity backsplash was not installed. All other vanities have been installed.
 - Observed 1 vanity with significant damage to the top.
- 4th Floor: 95% Complete
 - All vanities have been installed.

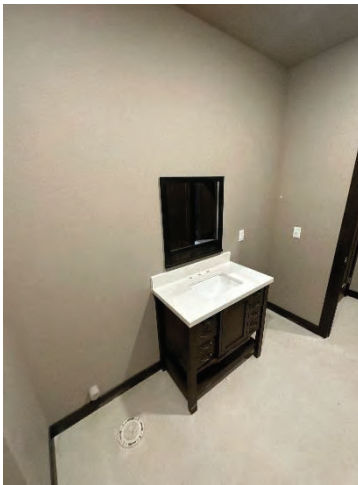

4th Floor Unit, Typical Install




4th Floor Unit, Damaged Sink

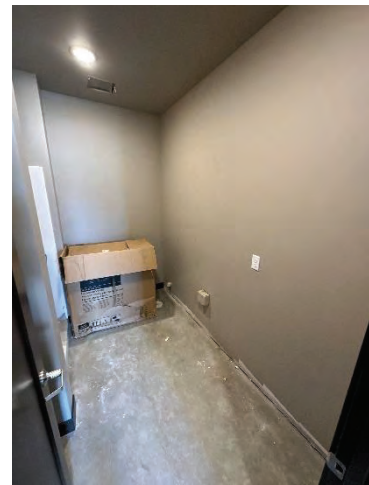

2nd Floor Unit



3rd Floor Unit, Damaged Top

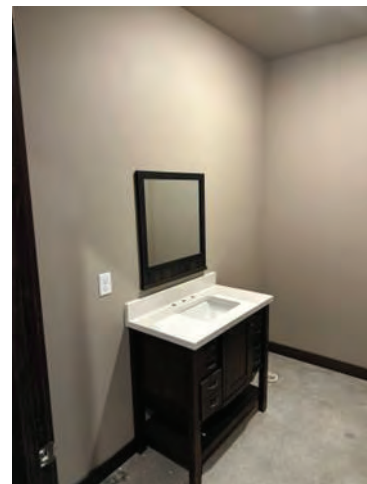

2nd Floor Unit, Typical Install

MOISTURE PROTECTION

Approximate Progress: 95% Complete


- All roofing membrane at the high roof and low roof on the west side of the building appeared to be installed. Status of roofing warranty and final inspection documents unknown.
- Low roof on the southeast corner of the building EPDM completed. The roof cap has not been completed.
- All roofing detailing, flashing and metal roof cap appeared to be installed at the time of the inspection.
- No significant ponding of any water on the roof present at the time of the inspection.

Potential Deficiencies:

- Excess materials and dunnage located on the roof to be removed.
- Observed several locations of soft spots in the roofing surface, possibly due to gaps in the coverboard.
- Observed several locations of cuts and damage to the low roof on the west side of the building.
- Observed areas of roof that were not draining properly and was holding approx. 1" of water.



Observed standing water in this location

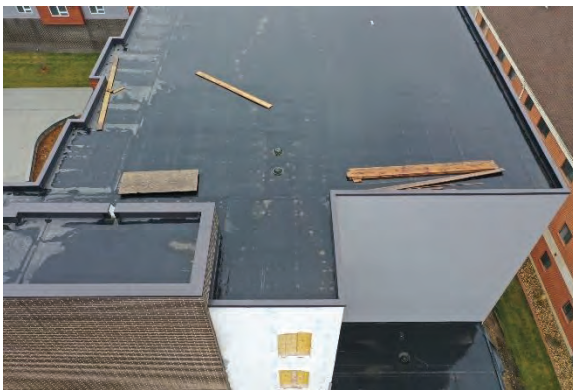

MASONRY

Approximate Progress: 80% Complete.

- North Elevation of the building to be completed. Only 3 courses of brick are currently installed.
- Joint sealant at all control joints to be completed.




METAL SIDING/METAL PANELS

Approximate Progress: 60% Complete.

- North Elevation of the building to be completed.
- East Elevation of the building to be completed.
- Soffit panels missing at west low roof.
- Flashing and metal returns at all doors and garage openings need to be completed.
- Observed multiple pallets of metal panels on site on 1st floor, did not perform quantitative analysis to verify enough materials were on site to complete. The approximate percent complete assumes that all materials are on site to complete.

Potential Deficiencies:

- Observed numerous areas where 3M flashing tape was applied to the face of the metal panels. The reasoning for the application of the tape was unable to be determined.
- Observed panels that were falling off or removed from the building at the interior corner of the west elevation of the building.



COMMERCIAL DOORS/FRAMES/HARDWARE

Approximate Progress: 50% Complete.

- All door, frame, and hardware at the stair towers need to be installed.
- All door, frame, and hardware in the trash rooms needs to be installed.

Potential Deficiencies:

- A detailed inspection of the components of each of the exterior doors was not completed as a part of this site inspection.



VINYL WINDOWS (SUPPLY ONLY)

Approximate Progress: 95% Complete.

- Observed 4 windows to be installed.
- Observed multiple windows stocked on 1st floor, possibly for replacement of damaged window panes and frames.

Potential Deficiencies:

- Observed approx. 10-15 windows with either broken or missing glass.
- Observed approx. 12-17 windows with broken or malfunctioning latches and/or cranks.
- Observed approx. 6-10 window frames that appeared to be warped or not leveled, causing operation issues.

GLASS & GLAZING

Approximate Progress: 95% Complete.

- All frames appeared to be installed.

DRYWALL

Approximate Progress: 75% Complete

- 1st Floor:
 - All elevator openings need to be completed.
- 2nd Floor: 75% Complete
 - Observed 2 units where drywall needed to be completed throughout the unit.
 - Observed 1 unit with significant touch ups and repair required.
 - Observed several locations where drywall repair due to other trade activities required.
 - Observed several locations where drywall repair due to water damage is required (see Section GENERAL W&L ROUGH CARPENTRY LABOR for more detail).
- 3rd Floor: 80% Complete
 - Observed 1 unit with significant touch ups and repair required.
 - Observed several locations where drywall repair due to other trade activities required.
 - Observed several locations where drywall repair due to water damage is required (see Section GENERAL W&L ROUGH CARPENTRY LABOR for more detail).
- 4th Floor: 90% Complete
 - Observed several locations where drywall repair due to other trade activities required.
 - Observed several locations where drywall repair due to water damage is required (see Section GENERAL W&L ROUGH CARPENTRY LABOR for more detail).



2nd Floor Unit



2nd Floor Unit



2nd Floor Unit



2nd Floor Unit, Several Locations



4th Floor Unit, Several Locations

CARPET

Approximate Progress: 25% Complete

- 2nd Floor: 0% Complete
 - Observed no units with any carpeting installed or stocked within the unit.
- 3rd Floor: 0% Complete
 - Observed no units with any carpeting installed or stocked within the unit.
- 4th Floor: 80% Complete
 - Observed 2 units without any carpeting installed or stocked within the unit.



4th Floor Unit




4th Floor Unit

PAINTING/STAINING

Approximate Progress: 70% Complete


- 1st Floor: 0% Complete
 - The public restroom area needs to be completed.
 - Stair towers need to be completed.
- 2nd Floor: 90% Complete
 - Observed 2 units that needed significant painting completed.
 - Most of the units require only small touch ups to complete.
- 3rd Floor: 90% Complete
 - Observed 1 unit that needed significant painting completed.
 - Most of the units require only small touch ups to complete.
- 4th Floor: 80% Complete
 - Most of the units require only small touch ups to complete.
 - Lobby and elevator openings need to be completed.



3rd Floor Unit



4th Floor Unit

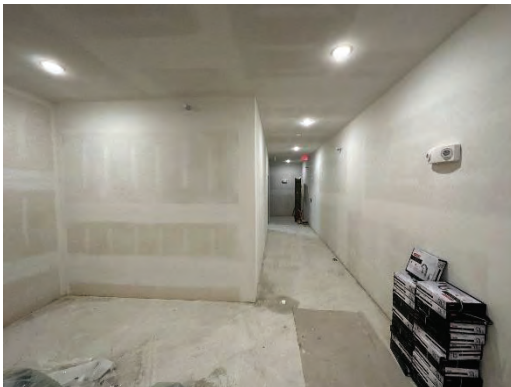

4th Floor Lobby

FILL NAIL HOLES

Approximate Progress: Approximately 75% Complete

- 2nd Floor: 0% Complete,
 - No nail holes have been filled on the floor.
- 3rd Floor: 95% Complete
 - Observed only a few locations where work was missed or not completed. Only punch List related items remaining
- 4th Floor: 95% Complete
 - Observed only a few locations where work was missed or not completed. Only punch List related items remaining

POSTAL SPECIALTIES/BIKE RACK/DOOR MARKERS

Approximate Progress:

- 1st Floor:
 - No postal specialties installed.
 - Materials were stored on site.

FIRE EXTINGUISHERS & CABINETS

Approximate Progress: 0% Complete – Did not observe any stored materials on site.

- 1st Floor: 0% Complete
 - Did not observe storage of any materials on site to be installed.
- 2nd Floor: 0% Complete
 - No fire extinguisher or Fire Extinguisher cabinets were installed.
- 3rd Floor: 0% Complete
 - No fire extinguisher or Fire Extinguisher cabinets were installed.
- 4th Floor: 0% Complete
 - No fire extinguisher or Fire Extinguisher cabinets were installed.

Potential Deficiencies:

- Observed floor to accessibility height of fire extinguishers to be higher than typical. This will need to be reviewed with the local building official to determine if the height will need to be adjusted.
- Observed fire extinguisher cabinet openings to be absent of sheetrock on the inside of the opening. If standard fire extinguisher cabinets are used, this may need to be sheet rocked to maintain corridor fire rating. Alternatively, fire rated cabinets may be able to be used. Review with local building officials necessary to confirm.



4th Floor Lobby



3rd Floor Lobby

CEILING FANS

Approximate Progress: 95% Complete

- 2nd Floor: 95% Complete
 - Observed ceiling fans installed in all units. Only minor (if any) punch list items remain.
- 3rd Floor: 95% Complete
 - Observed ceiling fans installed in all units. Only minor (if any) punch list items remain.
- 4th Floor: 95% Complete
 - Observed ceiling fans installed in all units. Only minor (if any) punch list items remain.



3rd Floor Unit



3rd Floor Unit



4th Floor Unit



4th Floor Unit

CLOSET SHELVING

Approximate Progress: 0% Complete

- 2nd Floor: 0% Complete
 - Observed none of the shelving installed throughout the floor.
- 3rd Floor: 0% Complete
 - Observed none of the shelving installed throughout the floor.
- 4th Floor: 0% Complete
 - Observed none of the shelving installed throughout the floor.

TOILETS AND ACCESSORIES

Approximate Progress: 50% Completed

- 1st Floor:
 - Observed toilets stored on site. Did not confirm quantity.
- 2nd Floor: 0% Complete
 - No toilets installed throughout the floor in any unit.
- 3rd Floor: 0% Complete
 - No toilets installed throughout the floor in any unit.
- 4th Floor:
 - No toilets installed throughout the floor in any unit.

APPLIANCES & AC UNITS

Approximate Progress: 20% Completed

- 1st Floor:
 - Did not observe any stored appliances on 1st floor.
- 2nd Floor: 0% Complete
 - Observed all AC units missing throughout the floor.
 - Observed all washer and dryers missing from the units.
 - Observed all dishwashers missing from the units.
 - Observed all ranges and refrigerators missing from the units.
- 3rd Floor: 0% Complete
 - Observed all AC units missing throughout the floor.
 - Observed all washer and dryers missing from the units.
 - Observed all dishwashers missing from the units.
 - Observed all ranges and refrigerators missing from the units.
- 4th Floor: 50% Complete
 - Observed all AC units stocked in each unit, not installed.
 - Observed all washer and dryers missing from the units.
 - Observed all dishwashers stocked in each unit, not installed.
 - Observed all ranges and most refrigerators stocked in each unit, not installed.




2nd Floor Unit, Typical




3rd Floor Unit, Typical



4th Floor Unit, Typical



4th Floor Unit, Typical



4th Floor Unit, Typical


KITCHEN SINKS/FAUCETS

Approximate Progress: 5% Complete

- 2nd Floor: 5% Complete
 - Observed one 1 unit with the sink set in place in the kitchen.
 - Observed all units without the sinks hooked up.
- 3rd Floor: 0% Complete
 - Observed all units without the sinks stocked or hooked up.
- 4th Floor: 0% Complete
 - Observed all units without the sinks stocked or hooked up.



4th Floor Unit, Typical



4th Floor Unit, Typical

BATH FAUCETS/SHOWER HEADS

Approximate Progress: 0% Complete


- 2nd Floor: 0% Complete
 - Observed all units where plumbing faucets and shower heads were not installed.
- 3rd Floor: 0% Complete
 - Observed all units where plumbing faucets and shower heads were not installed.
- 4th Floor: 0% Complete
 - Observed all units where plumbing faucets and shower heads were not installed.



2nd Floor Unit, Typical



3rd Floor Unit, Typical




4th Floor Unit, Typical

BATHROOM MIRRORS

Approximate Progress: Approximately 80% Complete


- 2nd Floor: 75% Complete
 - Observed 3 units where mirror was not installed.
- 3rd Floor: 95% Complete
 - All mirrors throughout the floor have been installed. Only punch list items remain.
- 4th Floor: 95% Complete
 - All mirrors throughout the floor have been installed. Only punch list items remain.



2nd Floor Unit



2nd Floor Unit



4th Floor Unit

WINDOW TREATMENTS

Approximate Progress: 0% Complete

- 2nd Floor: 0% Complete
 - None of the window treatments have been installed.
- 3rd Floor: 0% Complete
 - None of the window treatments have been installed.
- 4th Floor: 0% Complete
 - None of the window treatments have been installed.

CONVEYING SYSTEMS

Approximate Progress: 90% Complete

- 1st Floor:
 - Elevator equipment installed and hooked up. The elevator was not in service at the time of inspection.
- 2nd Floor:
 - The drywall finishes to be completed around elevator door.
- 3rd Floor:
 - The drywall finishes to be completed around elevator door.
- 4th Floor:
 - The drywall finishes to be completed around elevator door.



4th Floor Unit


BUILDING SPRINKLER

Approximate Progress: 90% Complete

- 1st Floor: 90% Complete
 - Main piping and distribution completed.
 - Riser pipe and valves installed and wired.
 - Final inspection tags not completed.
- 2nd Floor: 90% Completed with trim out.
 - Observed majority of sprinkler heads trimmed out in the units, a few that were incomplete.
- 3rd Floor: 90% Completed with trim out.
 - Observed majority of sprinkler heads trimmed out in the units, a few that were incomplete.
- 4th Floor: 90% Completed with trim out.
 - Observed majority of sprinkler heads trimmed out in the units, a few that were incomplete.



2nd Floor Unit



2nd Floor Unit, Typical



1st Floor Mechanical


PLUMBING

Approximate Progress: 50% Complete


- 1st Floor: 5% Complete
 - All PVC needs to be tied in and hooked up to building sanitary.
 - No fire collars have been installed.
 - Plumbing rough in and fixtures need to be completed in the 1st floor common bathroom area.
- 2nd Floor: 60% Complete
 - Observed 2 units where showers were not installed. They were stocked in units.
 - None of the toilets have been installed.
 - No water to any unit, all rough-in is assumed to be completed and inspected.
- 3rd Floor: 75% Complete
 - None of the toilets have been installed.
 - No water to any unit, all rough-in is assumed to be completed and inspected.
- 4th Floor: 75% Complete
 - None of the toilets have been installed.
 - No water to any unit, all rough-in is assumed to be completed and inspected.



2nd Floor Unit



2nd Floor Unit




2nd Floor Unit, Typical Condition



3rd Floor Unit, Typical Condition



1st Floor

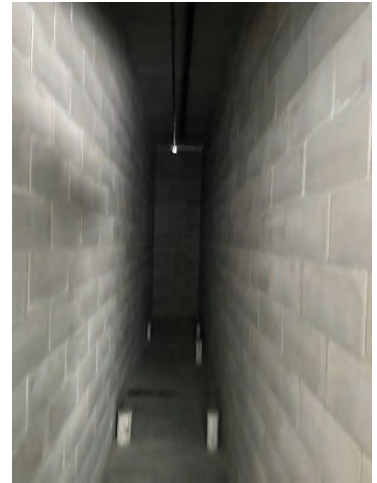

1st Floor, Plumbing Chase


HVAC

Approximate Progress: 75% Complete.

- 1st Floor: 60% Complete
 - Sealant at all exterior louvers needs to be completed.
 - Bathroom HVAC needs to be completed.
- 2nd Floor: 90% Complete
 - Observed all units to be missing the bath fan trim cover.
- 3rd Floor: 90% Complete
 - Observed all units to be missing the bath fan trim cover.
- 4th Floor: 90% Complete
 - Observed all units to be missing the bath fan trim cover.



2nd Floor Unit, Typical Condition



3rd Floor Unit, Typical Condition



1st Floor, HVAC Incomplete

ELECTRICAL/SECURITY SYSTEM

Approximate Progress: 90% Complete

- 1st Floor: 90% Complete
 - Observed potential concern with shaft rating for electrical feeder wire.
 - Observed potential concern with clearance and proximity to fire sprinkler piping.
- 2nd Floor: 90% Complete
 - Observed majority electrical devices installed throughout the floor, regardless of finishes.
 - Panels are labeled but did not have final sign off stamp.
- 3rd Floor: 90% Complete
 - Observed majority electrical devices installed throughout the floor, regardless of finishes.
 - Panels are labeled but did not have final sign off stamp.
- 4th Floor: 90% Complete
 - Observed majority electrical devices installed throughout the floor, regardless of finishes.
 - Panels are labeled but did not have final sign off stamp.



2nd Floor Unit




2nd Floor Unit, Typical Condition



3rd Floor Unit, Typical Condition



3rd Floor Unit, Typical Condition

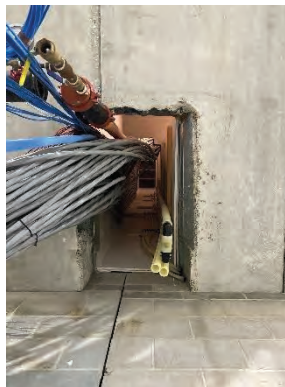

1st Floor Shaft



1st Floor Electrical Gear


PAVING AND SIDEWALKS

Approximate Progress: 75% Complete

- North Elevation: Approximately 95% Complete
 - Additional work includes pouring the walk door stoop pad and setting bollards at the edges of the garage doors.
- East Elevation: Scope unknown
- South Elevation: Approximately 10% Complete
 - Concrete curb, gutter and sidewalk along E Kemp Avenue needs to be completed.
 - Asphalt patching from existing street to new curb to be completed.
- West Elevation: Approximately 95% Complete
 - All sidewalk and stoop pads have been completed, all concrete in and around the plaza area appears to be completed.

Potential Deficiencies:

- Did not perform detailed inspection of the pavement for chips, cracks, and damage from construction.
- North Elevation - Elevation of the concrete alley does not match the elevation of the finished floor of the building. Concrete removal and replacement work is necessary to allow for proper transition of grade from building to alley.



BID PACKAGES NOT APPLICABLE FOR THIS SITE INSPECTION

The following line items listed on the Sworn Construction Statement do not apply to this site observation report, either due to the inability to observe the completed work, the work was observed to be significantly completed, or not enough information was available to formulate an opinion on the status of the work.

- *General Conditions*
- *Testing & Inspections*
- *Foundation Removal*
- *Site Survey/Civil*
- *Building Demolition*
- *Concrete*
- *Asbestos*
- *Excavation*
- *Precast Concrete – Materials/Erection*
- *Move Utilities*
- *General W&L Rough Carpentry Materials*
- *General W&L Finish Carpentry Materials*
- *Wood Components/Trusses*
- *Sealants*
- *Overhead Garage Doors*
- *Accrued Interest*
- *Site Fencing/Accessories/Dumpster Enclosure*
- *Site Utilities*
- *Land*
- *Exterior Signage*
- *Building Insulation*

ADDITIONAL CONSIDERATIONS

Exterior Conditions:

- Observed potential roof leaks throughout the low roof due to penetrations and construction damage.
- Observed a few areas where the flashing from the brick to the roof cap and parapet wall could be areas of potential moisture concerns.

Interior Conditions:

- Observed the trash chute shaft with only 1 layer of sheet rock on each side of the wood framing. This could be an area of concern due to the possible requirement of a 2-hour rating at this shaft.
- Observed a vertical chase that contained electrical feeder wires, sprinkler piping, and water lines. This is an area of concern regarding the rating of the shaft extending more than 3 floors vertically.
- In our opinion, there is a concern with maintaining the two-hour rating at the stair tower door frames. A large gap was observed from the precast wall panel to the door frame opening.
- In our opinion, there is concern with the condition of the exterior sheathing and in-wall insulation at all locations where moisture was observed at the windows. In our opinion, there is also concern of mold present at these locations, which will need to be addressed.

APPENDIX 1 – UNIT SPECIFIC PUNCH LISTS



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704


Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items


#581: Complete door hardware

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#582: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#583: Complete flooring

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#584: Window latch broken

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#585: Repair water damaged drywall at windows

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024

Priority:

Status:

Initiated



#586: Drywall patch

Type:

Location:

2nd Floor>Fitness Center

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated





#587: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#588: Paint touch up

Type:	Location: 2nd Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

Fix once drywall is patched





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#691: Masonry infill at elevator door


Type:	Location: 2nd Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#692: Paint walls

Type:	Location: 2nd Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#693: Electrical incomplete A-C: Gehrtz Construction Reports Page 43 of 410

Type:

Location:

2nd Floor Hallway

Date Created:

Due Date:


04/17/2024**04/20/2024**

Priority:

Status:

Initiated

Description:

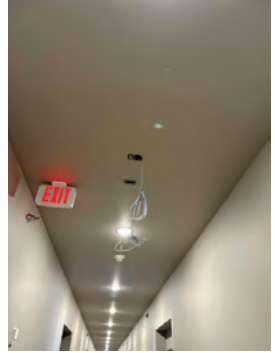**#694: Window pane broken**

Type:

Location:

2nd Floor Hallway


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

Description:

#695: Window missing

Type:

Location:

2nd Floor Hallway

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

Creator: Adam LaPlante
Reference:
Punch Item Manager: Adam LaPlante
Final Approver: Adam LaPlante
Ball in Court: Adam LaPlante (Gehrtz Construction Services)
Assignee Name:
Description:

#696: Drywall patch


Type: Location: 2nd Floor Hallway
Date Created: Due Date: 04/20/2024
04/17/2024
Priority: Status: Initiated

Description:







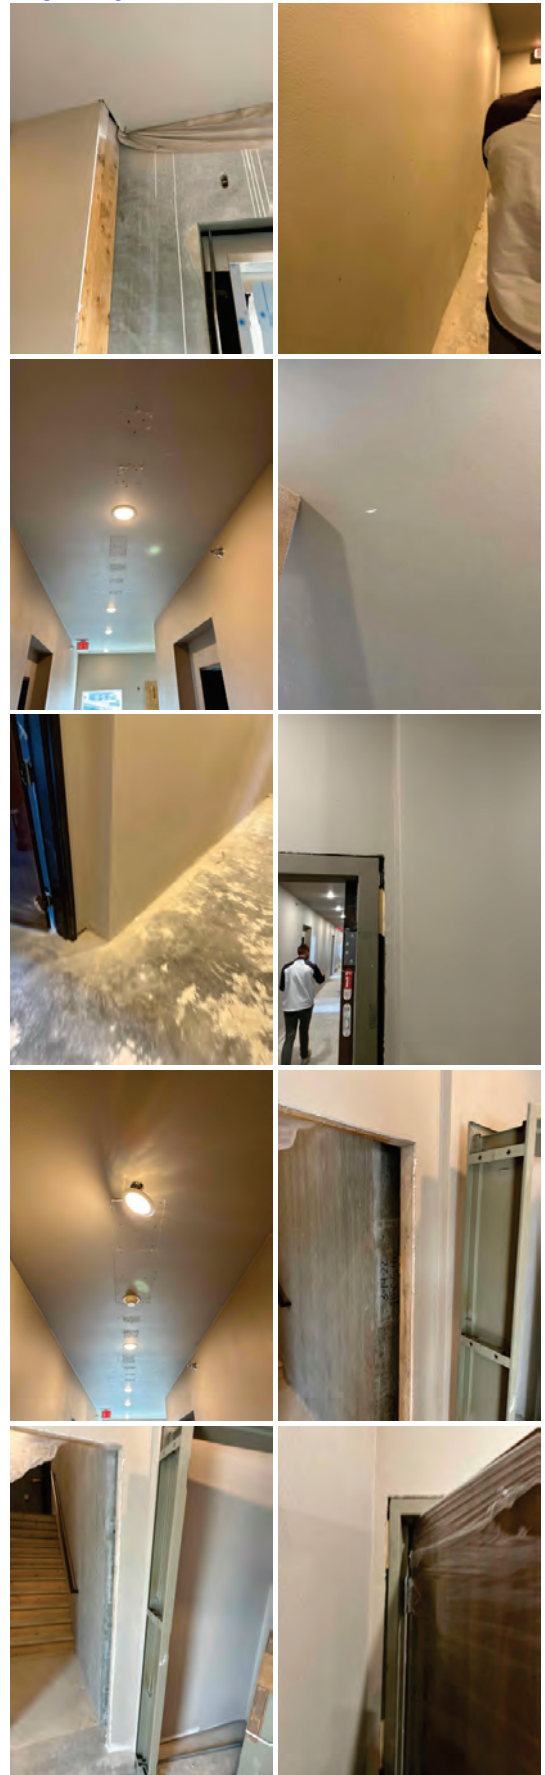



#697: Complete base

Type:

Location:

2nd Floor Hallway

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated

Description:

A-C: Gehrtz Construction Reports Page 49 of 410
#698: Complete door hardware

Type:

Location:

2nd Floor Hallway

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Description:



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

5 Items

#589: Electrical incomplete

Type:	Location: 2nd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#590: Fire stopping missing

Type:	Location: 2nd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#591: Complete door hardware

Type: Location:
2nd Floor>Mech/Jan't

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



Description:

#592: Complete flooring

Type: Location:
2nd Floor>Mech/Jan't

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated


Description:

#593: Complete cabinets, countertops, and trim

Type: Location:
2nd Floor>Mech/Jan't

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

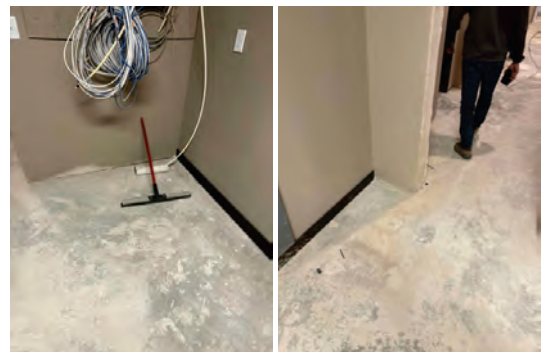

Description:



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

1 Items

#618: Drywall patch

Type:

Location:

2nd Floor>Roof Top Patio

Date Created:

Due Date:

04/17/2024


04/20/2024


Priority:

Status:

Initiated

Description:

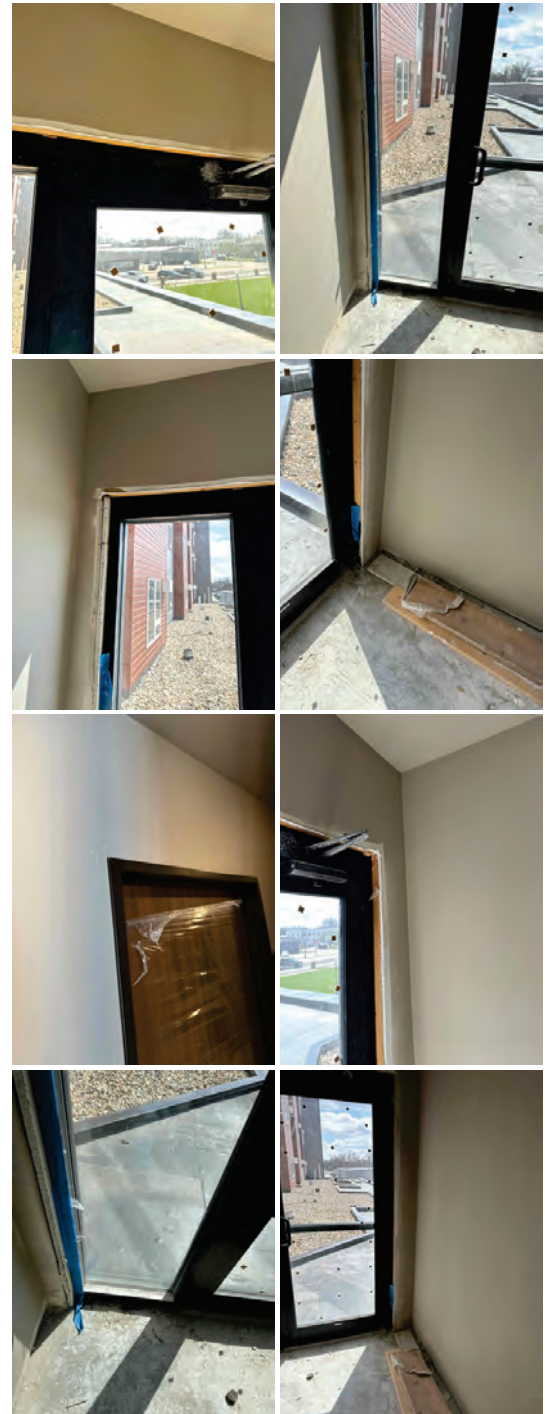

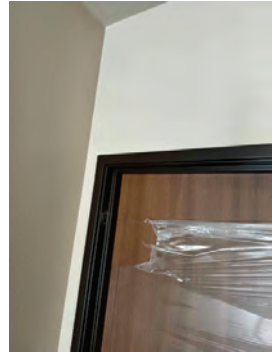



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

4 Items

#577: Complete door hardware

Type:	Location: 2nd Floor>Trash Chute
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#578: Drywall patch

Type:	Location: 2nd Floor>Trash Chute
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

Wall for trash chute doesn't meet 2-hour rating



#579: Complete flooring

Type:	Location: 2nd Floor>Trash Chute
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#580: Complete Mech/plumbing trim out

Type:

Location:

2nd Floor>Trash Chute

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

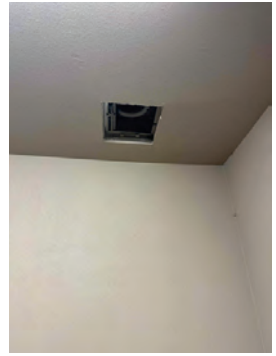

Description:



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#472: Electrical incomplete

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#473: Shelving Missing

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#477: Paint touch up

Type: Location:
2nd Floor>Unit 200

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#478: Chipped shower surround

Type: Location:
2nd Floor>Unit 200

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#480: Deliver & Install appliances

Type: Location:
2nd Floor>Unit 200

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#481: Complete door hardware

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#482: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#483: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#484: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#485: Complete flooring

Type:	Location: 2nd Floor>Unit 200
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#489: Drywall patch

Type:

Location:

2nd Floor>Unit 200

Date Created:

Due Date:




04/17/2024

04/20/2024

Priority:

Status:

Initiated

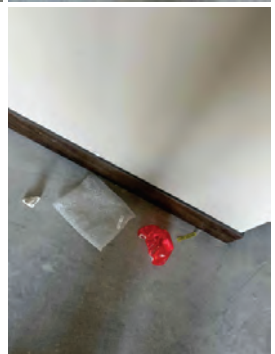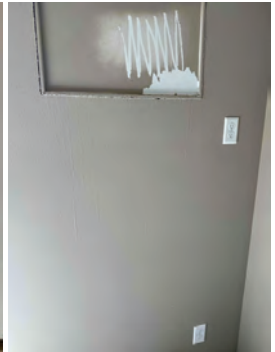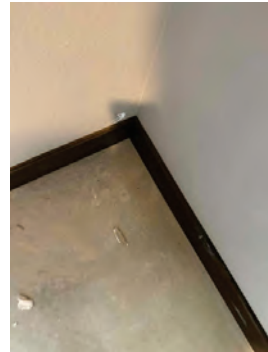



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#486: Electrical incomplete

Type:	Location: 2nd Floor>Unit 201
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#487: Shelving Missing


Type:	Location: 2nd Floor>Unit 201
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#488: Window pane broken in bedroom

Type: Location:
2nd Floor>Unit 201

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#490: Deliver & Install appliances

Type: Location:
2nd Floor>Unit 201

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#491: Complete cabinets, countertops, and trim

Type: Location:
2nd Floor>Unit 201

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#492: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 201
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#493: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 201
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#494: Complete flooring

Type:

Location:

2nd Floor>Unit 201

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#495: Drywall patch**

Type:

Location:

2nd Floor>Unit 201

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#512: Repair water damaged drywall at bedroom window**

Type:

Location:

2nd Floor>Unit 201

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated



#519: Clean up paint

Type:

Location:

2nd Floor>Unit 201

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

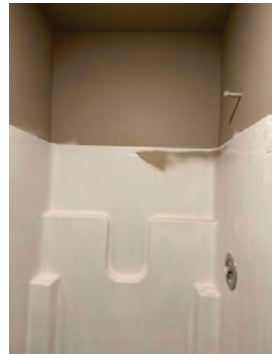



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#502: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#503: Complete door hardware

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#504: Complete cabinets, countertops, and trim

Type:

Location:

2nd Floor>Unit 202

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#505: Complete caulking at countertops & windows**

Type:

Location:

2nd Floor>Unit 202

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#506: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#507: Complete flooring

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#508: Drywall patch

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#516: Shelving Missing

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#517: Electrical incomplete

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated
Creator:	Reference:

#518: Paint touch up

Type:	Location: 2nd Floor>Unit 202
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

12 Items

#496: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#497: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#498: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#499: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#500: Complete flooring

Type:

Location:

2nd Floor>Unit 203

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#501: Drywall patch**

Type:

Location:

2nd Floor>Unit 203

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#509: Electrical incomplete**

Type:

Location:

2nd Floor>Unit 203

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#510: Shelving Missing

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#511: Window pane broken in bedroom

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#513: Window pane broken

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#514: Electrical incomplete

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#515: Shelving Missing

Type:	Location: 2nd Floor>Unit 203
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#537: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#538: Electrical incomplete

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#539: Shelving Missing

Type:

Location:

2nd Floor>Unit 204

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#540: Complete cabinets, countertops, and trim**

Type:

Location:

2nd Floor>Unit 204

Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:


Status:

Initiated



#541: Complete door hardware

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#542: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#543: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#544: Complete flooring

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#545: Drywall patch

Type:	Location: 2nd Floor>Unit 204
Date Created: 04/17/2024	Due Date: 04/20/2024

Priority:

Status:

Initiated



#564: Clean up paint

Type:

Location:

2nd Floor>Unit 204

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#520: Electrical incomplete

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#521: Shelving Missing

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#522: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#523: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#524: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#525: Complete flooring

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#528: Repair water damaged drywall at living room window

Type:	Location: 2nd Floor>Unit 205
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#531: Drywall patch

Type:

Location:

2nd Floor>Unit 205

Date Created:

Due Date:





04/17/2024

04/20/2024

Priority:

Status:

Initiated

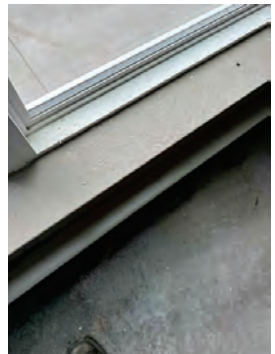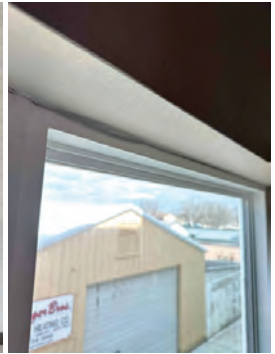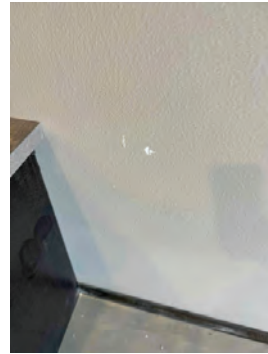



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#556: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#557: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#559: Electrical incomplete A-C: Gehrtz Construction Reports Page 89 of 410

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#560: Shelving Missing

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#561: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#562: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#563: Complete flooring

Type:	Location: 2nd Floor>Unit 206
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#565: Clean up paint

Type:

Location:

2nd Floor>Unit 206

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated



#568: Drywall patch

Type:

Location:

2nd Floor>Unit 206

Date Created:

04/17/2024


Due Date:

04/20/2024

Priority:

Status:

Initiated

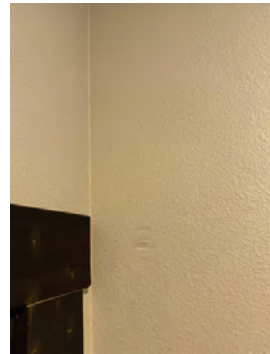



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#526: Electrical incomplete

Type:	Location: 2nd Floor>Unit 207
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#527: Shelving Missing

Type:	Location: 2nd Floor>Unit 207
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#529: Repair water damaged drywall at living room window

Type: Location:
2nd Floor>Unit 207

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#530: Deliver & Install appliances

Type: Location:
2nd Floor>Unit 207

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#532: Complete door hardware

Type: Location:
2nd Floor>Unit 207

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#533: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 207
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#534: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 207
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#535: Complete flooring

Type:

Location:

2nd Floor>Unit 207

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#536: Drywall patch**

Type:

Location:

2nd Floor>Unit 207

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#627: Electrical incomplete

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#628: Shelving Missing

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#630: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#631: Complete door hardware

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#632: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#633: Complete Mech/plumbing trim out


Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#634: Complete flooring

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#635: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#640: Drywall patch

Type:	Location: 2nd Floor>Unit 208
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#546: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#547: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#548: Complete door hardware

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#549: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#550: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#551: Complete flooring

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#552: Electrical incomplete

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#553: Shelving Missing

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#554: Repair water damaged drywall at living room window

Type:	Location: 2nd Floor>Unit 209
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#555: Drywall patch

Type:

Location:

2nd Floor>Unit 209

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#558: Repair water damaged drywall at bedroom window

Type:

Location:

2nd Floor>Unit 209

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#640: Shelving Missing

Type:	Location: 2nd Floor>Unit 210
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#645: Electrical incomplete

Type:	Location: 2nd Floor>Unit 210
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#647: Clean up paint

Type: Location:
2nd Floor>Unit 210

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#649: Deliver & Install appliances

Type: Location:
2nd Floor>Unit 210

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#650: Complete door hardware

Type: Location:
2nd Floor>Unit 210

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#651: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 210
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#652: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 210
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#653: Complete flooring

Type:

Location:

2nd Floor>Unit 210

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#654: Drywall patch**

Type:

Location:

2nd Floor>Unit 210


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

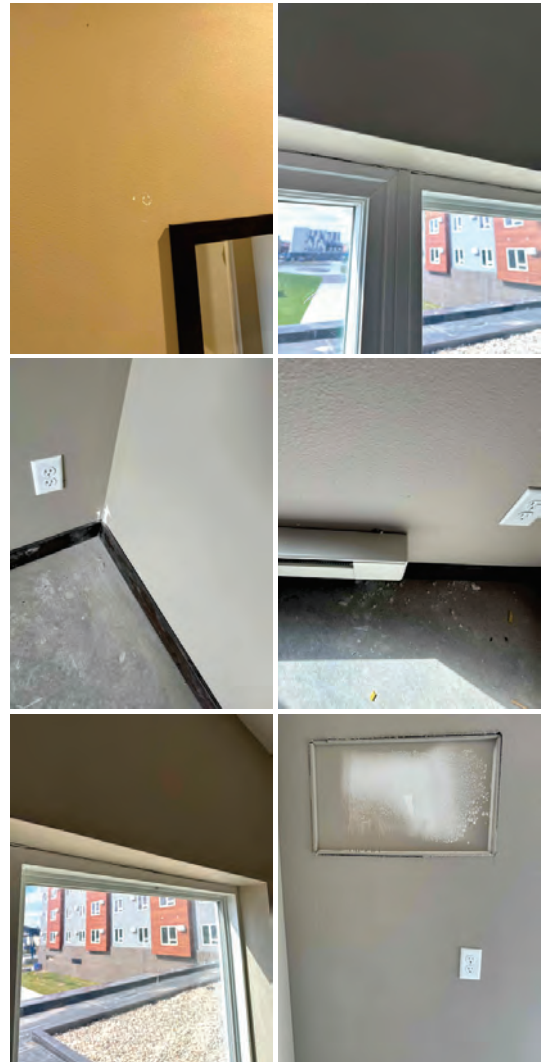Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704


Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#566: Electrical incomplete

Type:	Location: 2nd Floor>Unit 211
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#567: Shelving Missing

Type:	Location: 2nd Floor>Unit 211
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#569: Deliver & Install appliances

Type: Location:
2nd Floor>Unit 211

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#570: Paint touch up

Type: Location:
2nd Floor>Unit 211

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

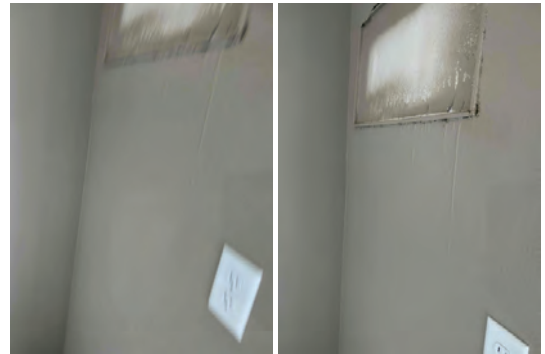


#571: Complete cabinets, countertops, and trim

Type: Location:
2nd Floor>Unit 211

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#572: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 211
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#573: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 211
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#574: Complete flooring

Type:

Location:

2nd Floor>Unit 211

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#575: Clean up paint

Type:

Location:

2nd Floor>Unit 211


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

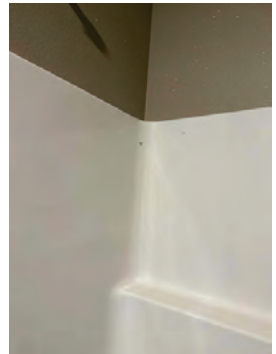Initiated

#576: Drywall patch

Type:

Location:

2nd Floor>Unit 211


Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

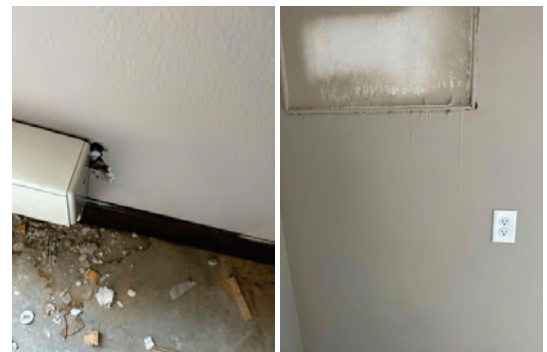Initiated

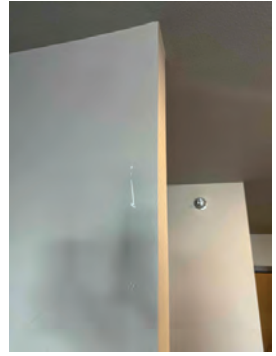



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#665: Electrical incomplete

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#666: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#667: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#668: Complete Mech/plumbing trim out


Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#669: Complete flooring

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#670: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#671: Sprinkler Escutcheons Missing

Type:	Location: 2nd Floor>Unit 212
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#672: Drywall patch

Type:

Location:

2nd Floor>Unit 212

Date Created:

Due Date:



04/17/2024

04/20/2024

Priority:

Status:

Initiated

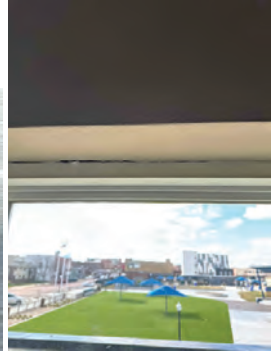



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

12 Items

#594: Electrical incomplete

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#595: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#596: Shelving Missing

Type:

Location:

2nd Floor>Unit 213

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#597: Complete caulking at countertops & windows

Type:

Location:

2nd Floor>Unit 213

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#598: Complete Mech/plumbing trim out

Type:

Location:

2nd Floor>Unit 213

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated



#599: Complete flooring

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#600: Repair water damaged drywall at both bedroom windows

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#601: Complete cabinets, countertops, and trim

Type:

Location:

2nd Floor>Unit 213

Date Created:

Due Date:


04/17/2024


04/20/2024

Priority:

Status:

Initiated

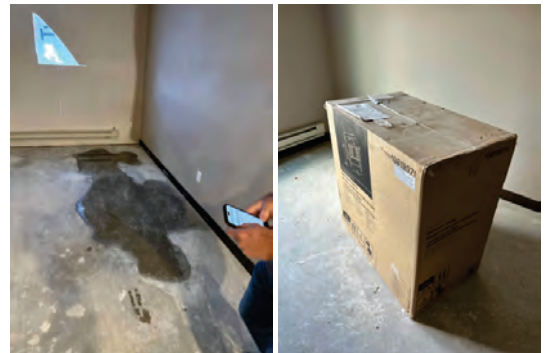

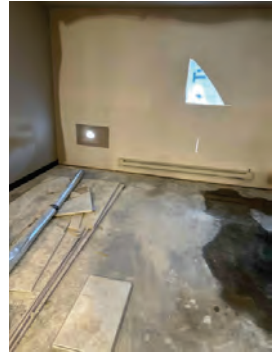

#602: Complete door hardware

Type: Location:
2nd Floor>Unit 213

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#603: Install window / window missing

Type: Location:
2nd Floor>Unit 213

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#604: Paint walls

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:
Once window is installed and drywall is patched

#605: Drywall patch

Type:	Location: 2nd Floor>Unit 213
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated







Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#682: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#683: Shelving Missing

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#685: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#686: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#687: Complete flooring

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#688: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 214
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#689: Window operable pane is warped

Type:

Location:

2nd Floor>Unit 214

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#690: Drywall patch

Type:

Location:

2nd Floor>Unit 214

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

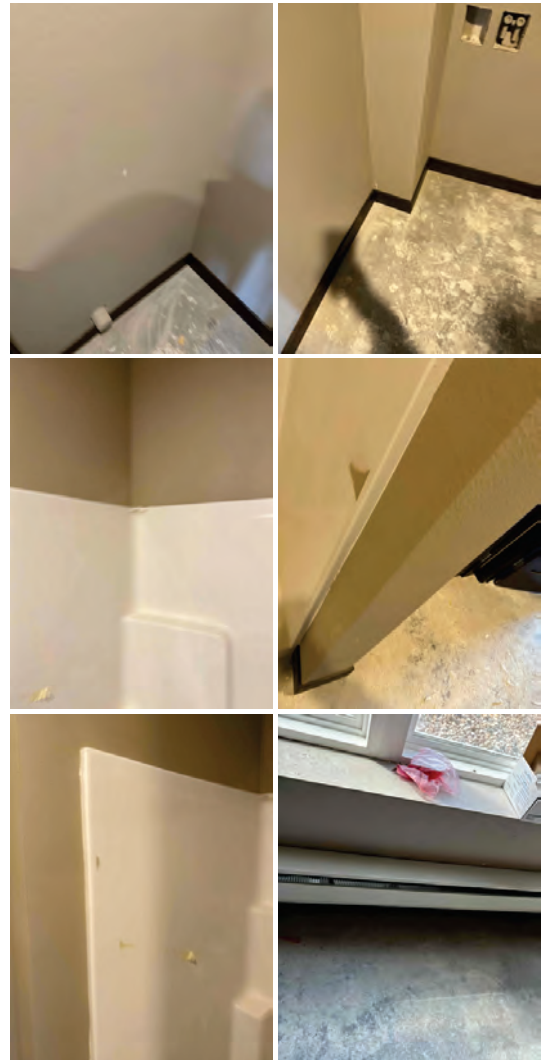





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#606: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#607: Shelving Missing

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#608: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#609: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#610: Complete flooring


Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#611: Electrical incomplete

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#612: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 215
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#613: Drywall patch

Type:

Location:

2nd Floor>Unit 215

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#614: Repair water damaged drywall at living room window

Type:

Location:

2nd Floor>Unit 215

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#615: Repair water damaged drywall at bedroom window

Type:

Location:

2nd Floor>Unit 215

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

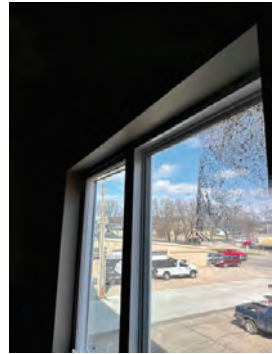



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#616: Shelving Missing

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#617: Electrical incomplete

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#619: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#620: Complete door hardware

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#621: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#622: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#623: Repair water damaged drywall at bedroom window

Type:	Location: 2nd Floor>Unit 217
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#624: Complete cabinets, countertops, and trim

Type: Location:
2nd Floor>Unit 217

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#625: Complete flooring

Type: Location:
2nd Floor>Unit 217

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#626: Repair water damaged drywall at living room window

Type: Location:
2nd Floor>Unit 217

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#629: Drywall patch

Type:

Location:

2nd Floor>Unit 217

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

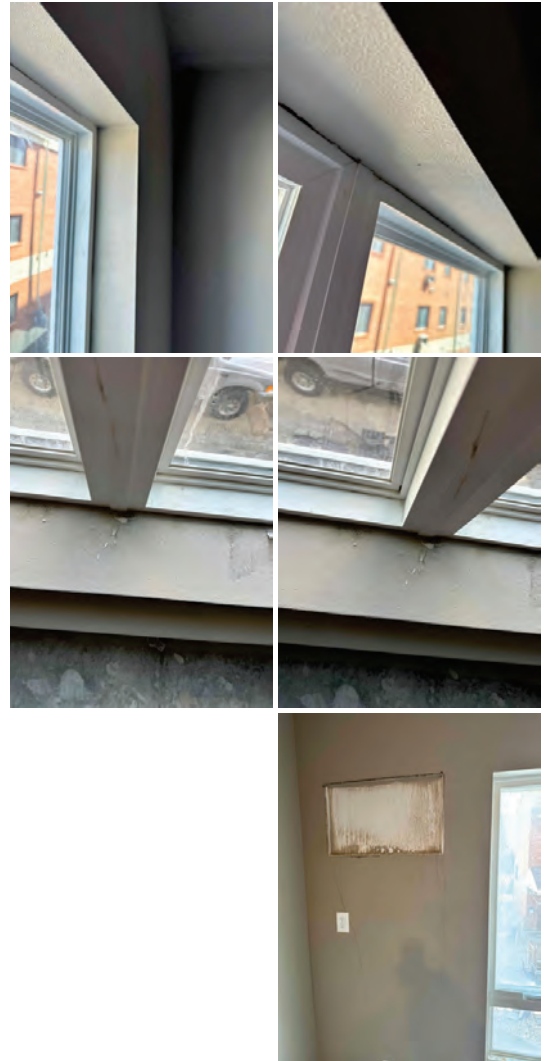



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#636: Electrical incomplete

Type:	Location: 2nd Floor>Unit 219
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#637: Shelving Missing

Type:	Location: 2nd Floor>Unit 219
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#638: Repair water damaged drywall at living room window

Type: Location:
2nd Floor>Unit 219

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#639: Repair water damaged drywall at bedroom window**

Type: Location:
2nd Floor>Unit 219

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#641: Deliver & Install appliances**

Type: Location:
2nd Floor>Unit 219

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#642: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 219
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#643: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 219
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#644: Complete flooring

Type:

Location:

2nd Floor>Unit 219

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#646: Complete cabinets, countertops, and trim

Type:

Location:

2nd Floor>Unit 219


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

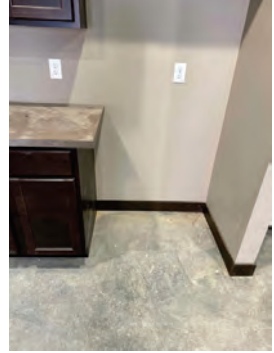Initiated

#648: Drywall patch

Type:

Location:

2nd Floor>Unit 219


Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

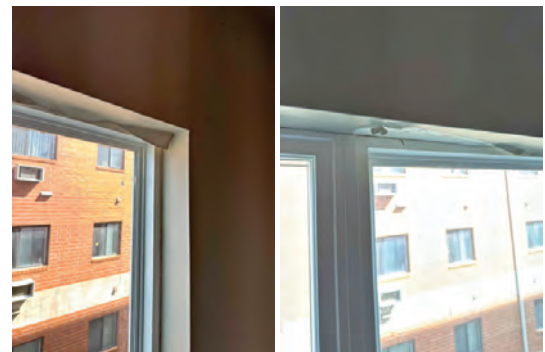Initiated

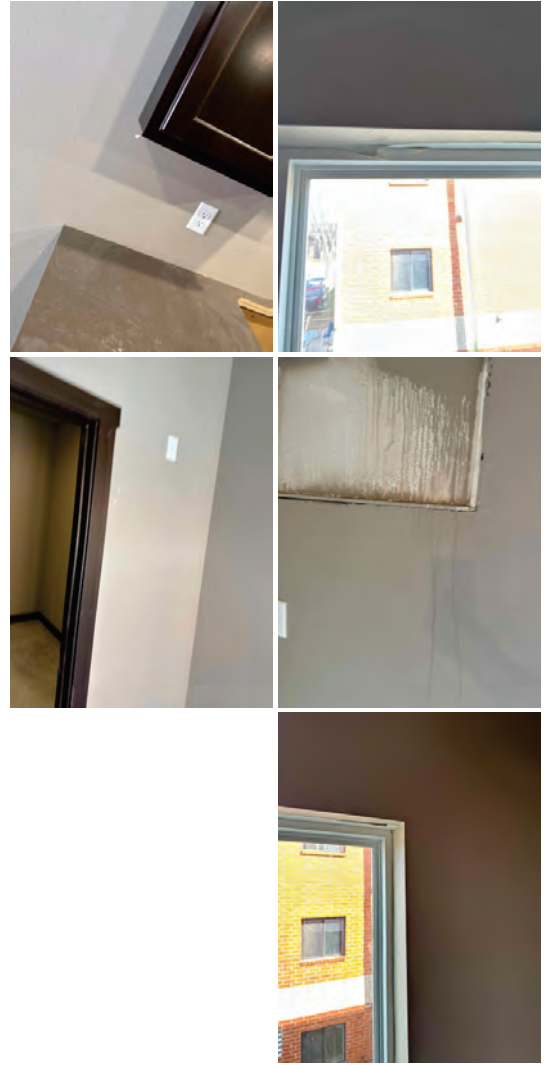



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#655: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#656: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#657: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#658: Complete flooring

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#659: Electrical incomplete


Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#660: Shelving Missing

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#661: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 221
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#662: Repair water damaged drywall at living room window

Type:

Location:

2nd Floor>Unit 221

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#663: Drywall patch

Type:

Location:

2nd Floor>Unit 221

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#664: Repair water damaged drywall at bedroom window

Type:

Location:

2nd Floor>Unit 221

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#673: Deliver & Install appliances

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#674: Complete caulking at countertops & windows

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#675: Complete Mech/plumbing trim out

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#676: Shelving Missing

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#677: Complete flooring


Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#678: Electrical incomplete

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#679: Complete cabinets, countertops, and trim

Type:	Location: 2nd Floor>Unit 223
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#679: Repair water damaged drywall at bedroom window

Type: Location:
2nd Floor>Unit 223

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#680: Repair water damaged drywall at living room window**

Type: Location:
2nd Floor>Unit 223

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated



**#681: Drywall patch**

Type: Location:
2nd Floor>Unit 223

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

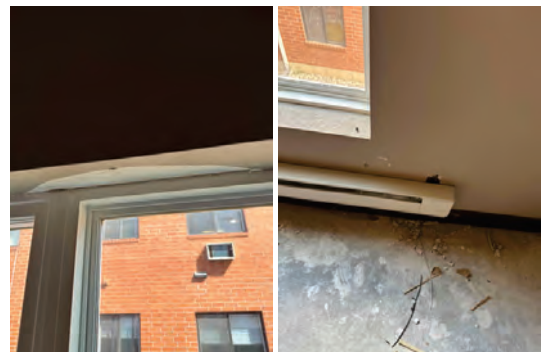

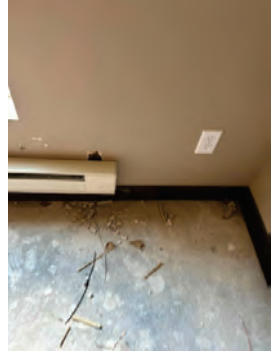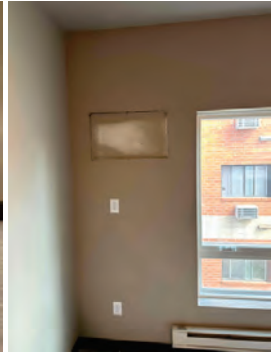



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#236: Complete flooring

Type:	Location: 3rd Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#237: Complete caulking at countertops & windows

Type:	Location: 3rd Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status:

Description:

#238: Complete base

Type: Location:
3rd Floor Hallway

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

Description:

#239: Fire Extinguisher Cabinet Missing - verify RO's meet code

Type: Location:
3rd Floor Hallway

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




Description:

#241: Electrical incomplete - empty boxes

Type: Location:
3rd Floor Hallway

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



Description:

#242: Paint door frame

Type:

Location:

3rd Floor Hallway

Date Created:

04/17/2024


Due Date:

04/20/2024

Priority:

Status:

Initiated

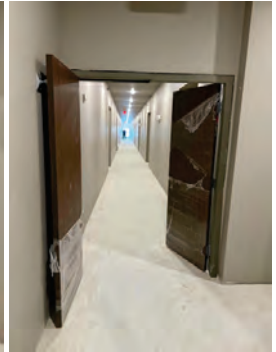

#243: Light fixture full of water - compromised

Type:

Location:

3rd Floor Hallway

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated



#244: Drywall patch

Type:

Location:

3rd Floor Hallway

Date Created:

Due Date:


04/17/2024

04/20/2024


Priority:


Status:

Initiated

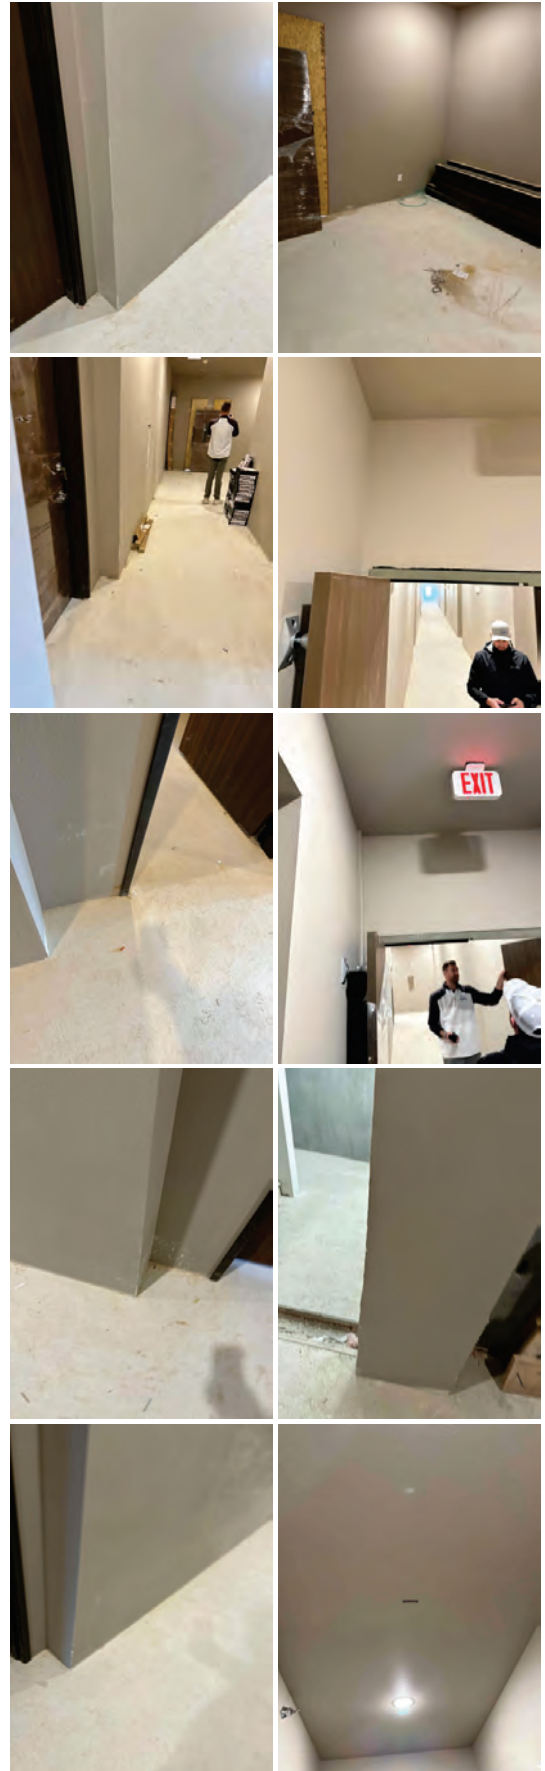



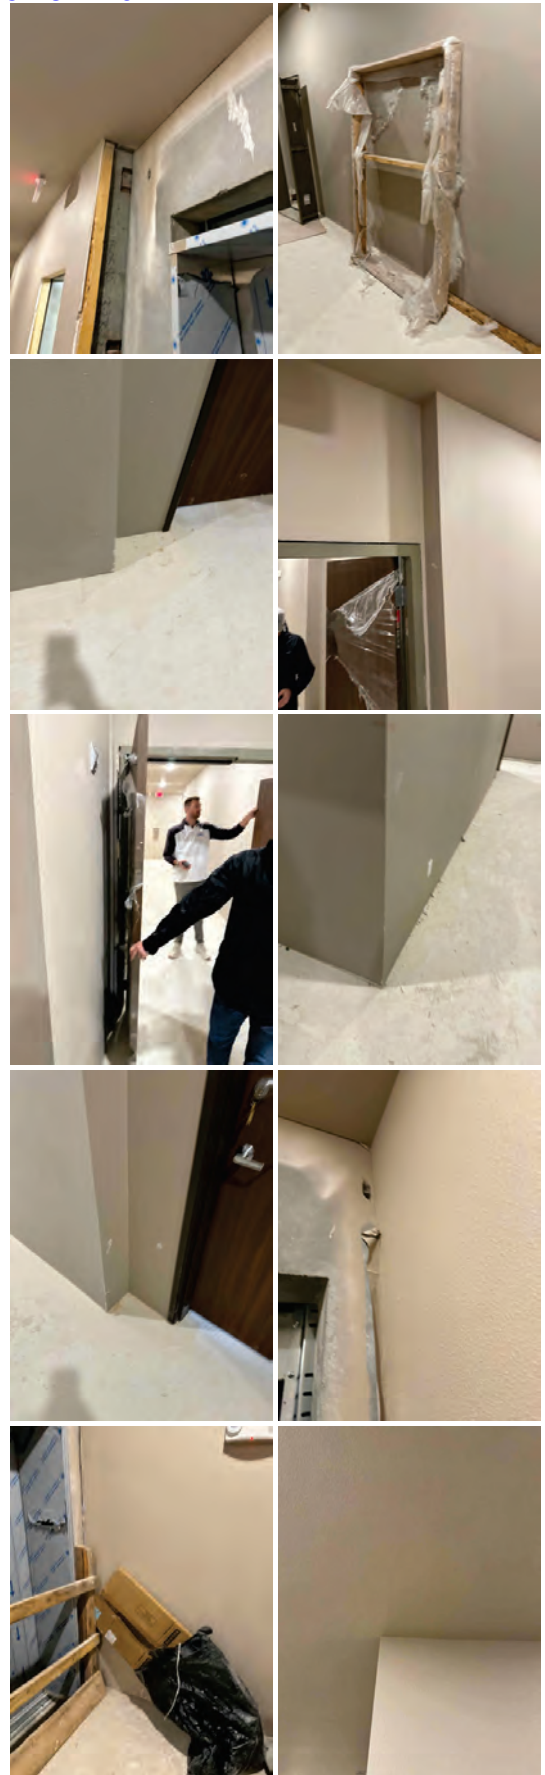

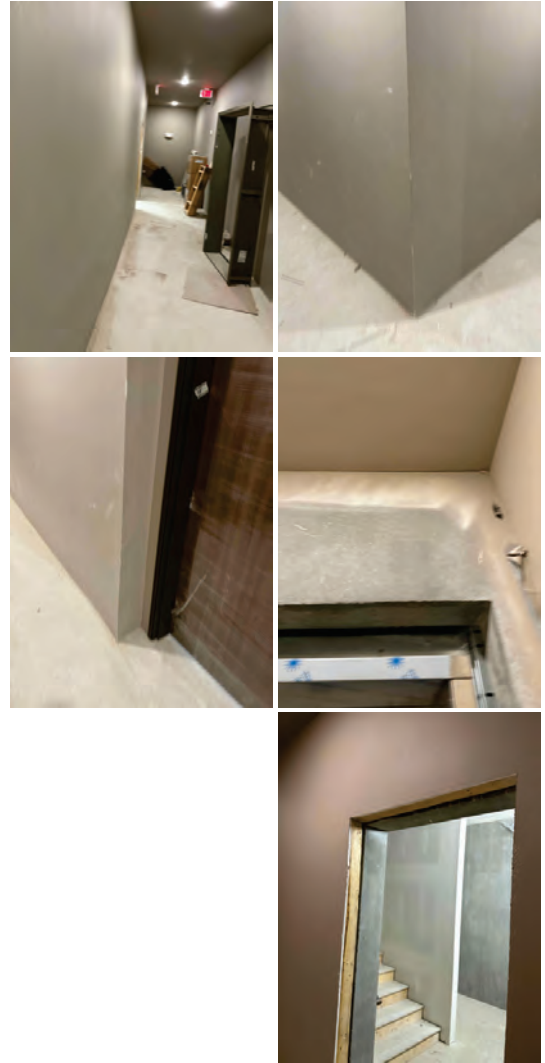

#245: Sprinkler Escutcheons Missing

Type:

Location:

3rd Floor Hallway

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#373: Paint door frame

A-C: Gehrtz Construction Reports Page 163 of 410

Type:

Location:

3rd Floor Hallway

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

5 Items


#364: Complete door hardware

Type:	Location: 3rd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status:



#366: Complete base

Type:	Location: 3rd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:

#367: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#370: Fire caulk penetrations

Type:	Location: 3rd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#371: Complete flooring

Type:	Location: 3rd Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

2 Items

#372: Drywall patch

Type:

Location:

3rd Floor>Trash Chute

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated

Description:

Wall does not meet 2-hour rating



#374: Install sprinkler head in trash chute

Type:

Location:

3rd Floor>Trash Chute

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#467: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#468: Shelving Missing

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Type: Location:
3rd Floor>Unit 300

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#470: Complete door hardware

Type: Location:
3rd Floor>Unit 300

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#471: Missing cover

Type: Location:
3rd Floor>Unit 300





Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#473: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#474: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status:

#475: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#476: Complete flooring

Type:	Location: 3rd Floor>Unit 300
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#479: Drywall patch

Type:

Location:

3rd Floor>Unit 300

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#455: Shelving Missing

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#456: Electrical incomplete

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#458: Deliver & Install appliances

Type: Location:
3rd Floor>Unit 301

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#459: Seal AC can

Type: Location:
3rd Floor>Unit 301

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#460: Repair water damaged drywall at bedroom window**

Type: Location:
3rd Floor>Unit 301

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#461: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#462: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#463: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#464: Complete flooring

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#465: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 301
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#466: Drywall patch

Type:

Location:

3rd Floor>Unit 301

Date Created:

Due Date:



04/17/2024

04/20/2024

Priority:

Status:

Initiated

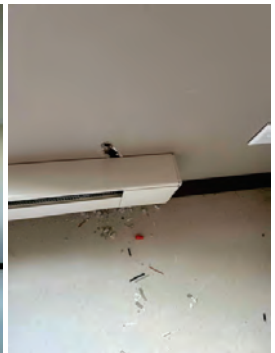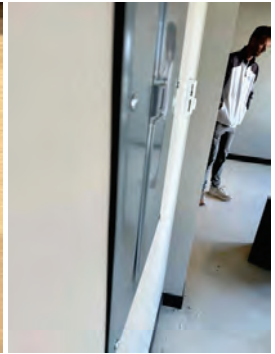



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#436: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#437: Electrical incomplete

Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#438: Complete door hardware

Type: Location:
3rd Floor>Unit 302

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#439: Shelving Missing

Type: Location:
3rd Floor>Unit 302

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#440: Seal AC can

Type: Location:
3rd Floor>Unit 302

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#441: Complete cabinets, countertops, and trim

Type:

Location:

3rd Floor>Unit 302

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#442: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#443: Complete Mech/plumbing trim out


Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#444: Complete flooring

Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#445: Drywall patch

Type:	Location: 3rd Floor>Unit 302
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#446: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#447: Electrical incomplete

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#448: Shelving Missing

Type:

Location:

3rd Floor>Unit 303

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#449: Seal AC can**

Type:

Location:

3rd Floor>Unit 303

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#450: Complete cabinets, countertops, and trim**

Type:

Location:

3rd Floor>Unit 303

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated



#451: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#452: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#453: Complete flooring

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#454: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 303
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#457: Drywall patch

Type:

Location:

3rd Floor>Unit 303

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#402: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#403: Shelving Missing

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Type: Location:
3rd Floor>Unit 304

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#405: Seal AC can

Type: Location:
3rd Floor>Unit 304

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#406: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 304

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#407: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#408: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#409: Complete flooring

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#410: Window operable frame is warped at bedroom

Type:	Location: 3rd Floor>Unit 304
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#411: Complete door hardware A-C: Gehrtz Construction Reports Page 193 of 410

Type: Location:
3rd Floor>Unit 304

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#412: Drywall patch

Type: Location:
3rd Floor>Unit 304

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

12 Items

#424: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 305
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#425: Electrical incomplete

Type:	Location: 3rd Floor>Unit 305
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#426: Shelving Missing

Type:

Location:

3rd Floor>Unit 305

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#427: Repair water damaged drywall at living room window

Type:

Location:

3rd Floor>Unit 305


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

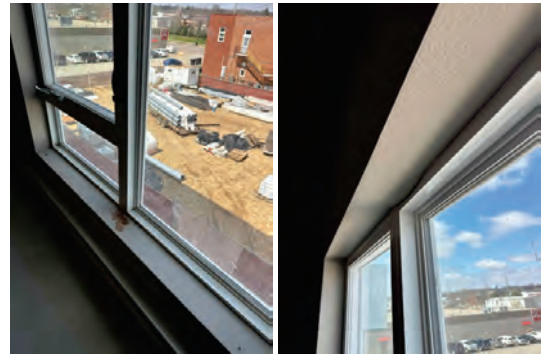Initiated

#428: Window operable frame is warped at living room

Type:

Location:

3rd Floor>Unit 305

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#429: Seal AC can

Type: Location:
3rd Floor>Unit 305

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#430: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 305

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#431: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 305
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#432: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 305
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#433: Complete flooring

Type:

Location:

3rd Floor>Unit 305

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#434: Paint touch up

Type:

Location:

3rd Floor>Unit 305

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#435: Drywall patch

Type:

Location:

3rd Floor>Unit 305

Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

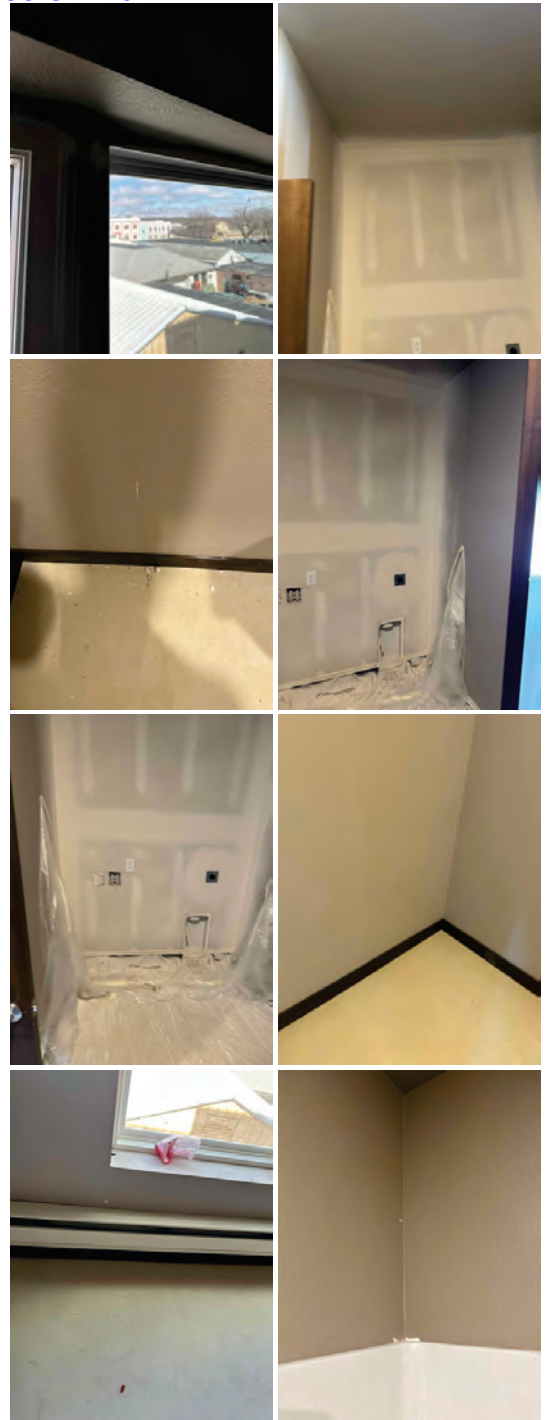



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

7 Items

#383: Electrical incomplete

Type:	Location: 3rd Floor>Unit 306
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#385: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 306
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#386: Shelving Missing

Type:

Location:

3rd Floor>Unit 306

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#387: Complete caulking at countertops & windows

Type:

Location:

3rd Floor>Unit 306

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#388: Complete Mech/plumbing trim out

Type:

Location:

3rd Floor>Unit 306

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#389: Complete flooring

Type:	Location: 3rd Floor>Unit 306
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#392: Drywall patch

Type:	Location: 3rd Floor>Unit 306
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#413: Electrical incomplete

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#414: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#415: Shelving Missing

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#416: Seal AC can

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#417: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#418: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#419: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#420: Complete flooring

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#421: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 307
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#422: Paint touch up

Type: Location:
3rd Floor>Unit 307

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#423: Drywall patch

Type: Location:
3rd Floor>Unit 307

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated







Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#322: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 308
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#323: Electrical incomplete


Type:	Location: 3rd Floor>Unit 308
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#324: Complete door hardware

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

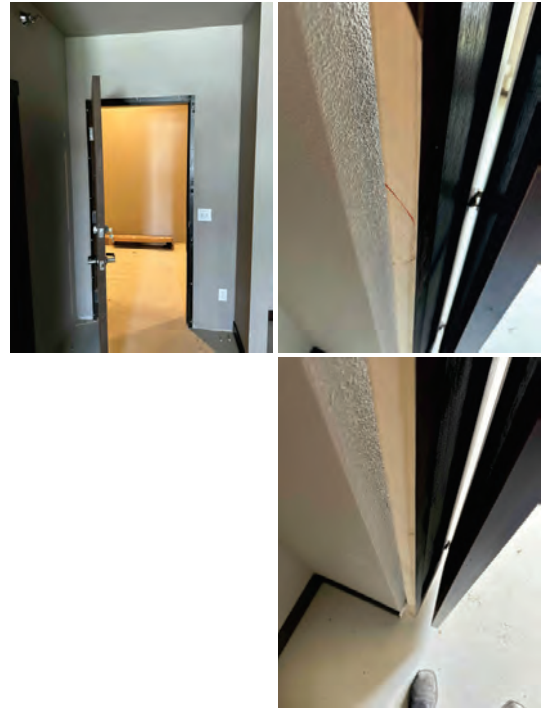**#325: Complete caulking at countertops & windows**

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#326: Shelving Missing

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#327: Window operable frame is warped at bedroom

Type:	Location: 3rd Floor>Unit 308
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#327: Seal AC can

Type:	Location: 3rd Floor>Unit 308
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#328: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#329: Complete Mech/plumbing trim out**

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#330: Complete flooring

Type: Location:
3rd Floor>Unit 308

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#331: Drywall patch

Type:

Location:

3rd Floor>Unit 308

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#390: Shelving Missing

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#391: Electrical incomplete

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#393: Deliver & Install appliances

Type: Location:
3rd Floor>Unit 309

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#394: Repair water damaged drywall at bedroom window

Type: Location:
3rd Floor>Unit 309

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#395: Seal AC can

Type: Location:
3rd Floor>Unit 309


Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#396: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#397: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#398: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#399: Complete flooring

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#400: Window frame broken in living room

Type:	Location: 3rd Floor>Unit 309
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#401: Drywall patch

Type:

Location:

3rd Floor>Unit 309

Date Created:

Due Date:



04/17/2024

04/20/2024

Priority:

Status:

Initiated

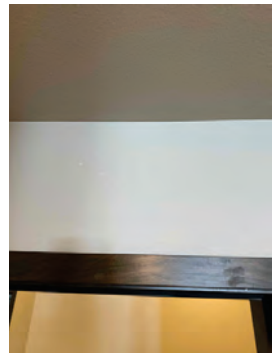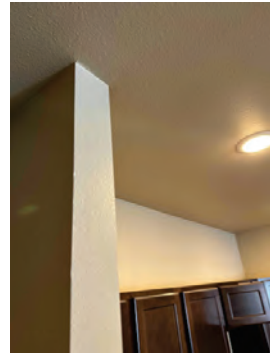



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#300: Shelving Missing

Type:	Location: 3rd Floor>Unit 310
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#301: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 310
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#302: Window Pane Broken in living room

Type: Location:
3rd Floor>Unit 310

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

**#303: Complete door hardware**

Type: Location:
3rd Floor>Unit 310

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#304: Window latch inoperable at living room**

Type: Location:
3rd Floor>Unit 310

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#305: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 310
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#306: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 310
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#307: Complete flooring

Type:

Location:

3rd Floor>Unit 310

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#308: Window operable frame is warped at bedrom

Type:

Location:

3rd Floor>Unit 310

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#309: Drywall patch

Type:

Location:

3rd Floor>Unit 310


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

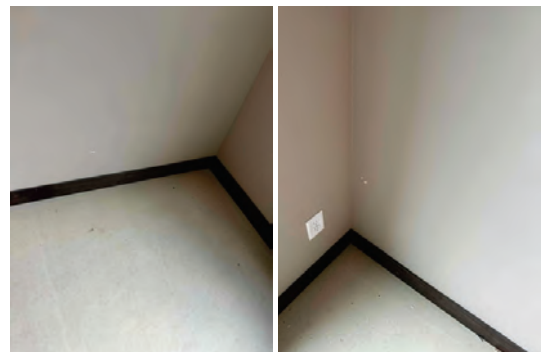Initiated

#310: Electrical incomplete

Type:

Location:

3rd Floor>Unit 310

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#375: Electrical incomplete

Type:	Location: 3rd Floor>Unit 311
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#376: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 311
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#377: Shelving Missing

Type:

Location:

3rd Floor>Unit 311

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#378: Complete caulking at countertops & windows

Type:

Location:

3rd Floor>Unit 311

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#379: Seal AC can

Type:

Location:

3rd Floor>Unit 311


Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

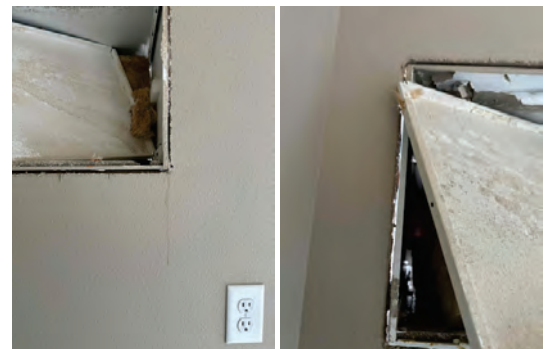Initiated

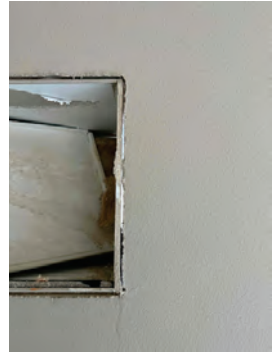

#380: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 311
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#381: Complete flooring

Type:	Location: 3rd Floor>Unit 311
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#382: Complete cabinets, countertops, and trim

Type:

Location:

3rd Floor>Unit 311

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#384: Drywall patch

Type:

Location:

3rd Floor>Unit 311

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#278: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#279: Electrical incomplete

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#280: Shelving Missing

Type:

Location:

3rd Floor>Unit 312

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#281: Window latch inoperable at bedroom

Type:

Location:

3rd Floor>Unit 312


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

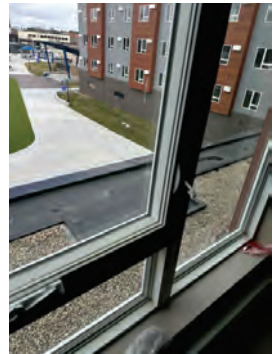Initiated

#282: Complete cabinets, countertops, and trim

Type:

Location:

3rd Floor>Unit 312


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:


Status:

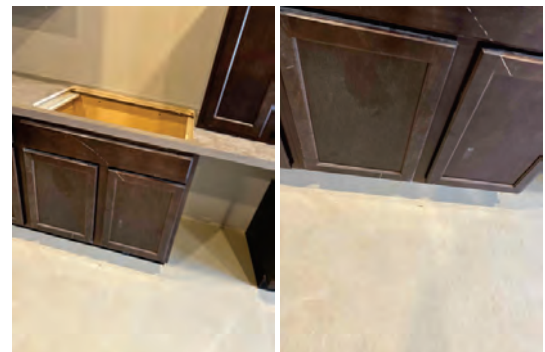Initiated



#283: Complete door hardware

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#284: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#285: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#286: Seal AC can

Type:	Location: 3rd Floor>Unit 312
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#287: Complete flooring

Type:

Location:

3rd Floor>Unit 312

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#288: Drywall patch

Type:

Location:

3rd Floor>Unit 312


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

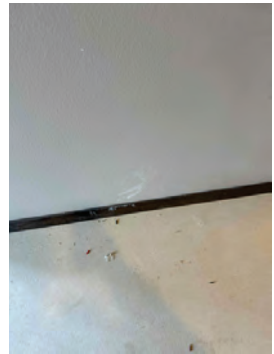Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#354: Electrical incomplete

Type:	Location: 3rd Floor>Unit 313
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#355: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 313
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#356: Complete door hardware

Type:

Location:

3rd Floor>Unit 313

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#357: Complete caulking at countertops & windows**

Type:

Location:

3rd Floor>Unit 313

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#358: Seal AC can

Type:

Location:

3rd Floor>Unit 313

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#359: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 313

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#360: Complete Mech/plumbing trim out**

Type: Location:
3rd Floor>Unit 313

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#361: Complete flooring

Type: Location:
3rd Floor>Unit 313

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#363: Drywall patch

Type:

Location:

3rd Floor>Unit 313

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated









Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#258: Electrical incomplete

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#259: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#260: Shelving Missing

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#261: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#262: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#263: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#264: Complete flooring

Type:	Location: 3rd Floor>Unit 314
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#265: Window operable frame is warped

Type: Location:
3rd Floor>Unit 314

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#266: Drywall patch

Type: Location:
3rd Floor>Unit 314

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#267: Complete door hardware

Type: Location:
3rd Floor>Unit 314

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

15 Items

#343: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#344: Electrical incomplete

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#345: Shelving Missing

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#346: Complete caulking at countertops & windows

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#347: Seal AC can

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#348: Window Pane Broken in bedroom

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#349: Repair water damaged drywall at bedroom window

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#350: Complete cabinets, countertops, and trim

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#351: Complete Mech/plumbing trim out**

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#352: Complete flooring

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#353: Drywall patch

Type:	Location: 3rd Floor>Unit 315
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#362: Window latch inoperable at living room

Type: Location:
3rd Floor>Unit 315

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#365: Repair water damaged drywall at living room window**

Type: Location:
3rd Floor>Unit 315

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#368: Repair water damaged drywall at bedroom window**

Type: Location:
3rd Floor>Unit 315

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#369: Shelving Missing

Type:

Location:

3rd Floor>Unit 315

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#332: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#333: Electrical incomplete

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#334: Shelving Missing

Type:

Location:

3rd Floor>Unit 317

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#335: Complete caulking at countertops & windows

Type:

Location:

3rd Floor>Unit 317

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#336: Seal AC can

Type:

Location:

3rd Floor>Unit 317

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated


#337: Repair water damaged drywall at bedroom window

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#338: Complete cabinets, countertops, and trim

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#339: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#340: Complete flooring

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#341: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 317
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#342: Drywall patch

Type:

Location:

3rd Floor>Unit 317

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

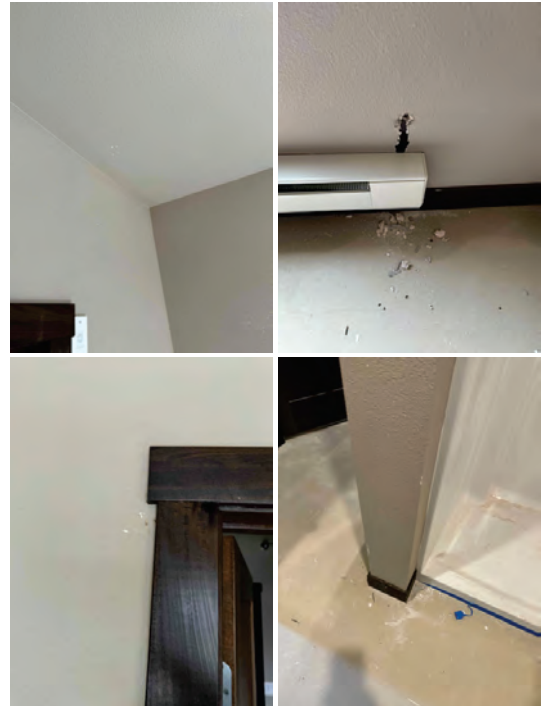



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#311: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#312: Electrical incomplete

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#313: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#314: Shelving Missing

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#315: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#316: Seal AC can

Type: Location:
3rd Floor>Unit 319

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#317: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 319

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#318: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#319: Repair water damaged drywall at bedroom window

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#320: Complete flooring

Type:	Location: 3rd Floor>Unit 319
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#321: Drywall patch

Type:

Location:

3rd Floor>Unit 319

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

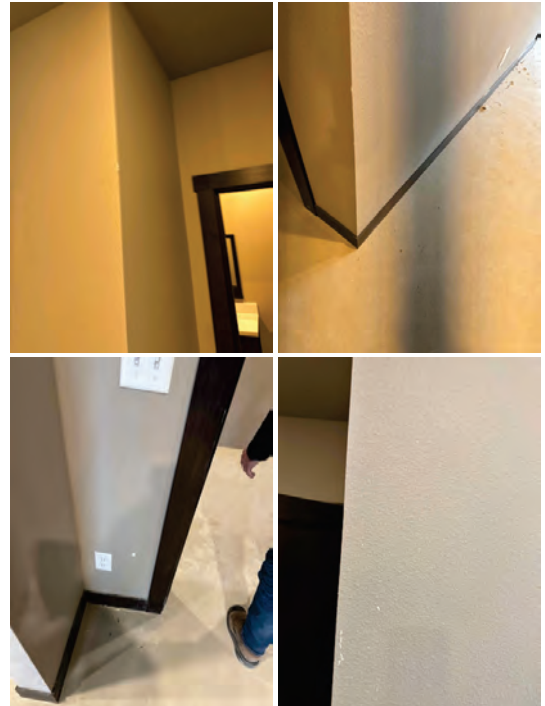



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#289: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#290: Shelving Missing

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#291: Electrical incomplete

Type: Location:
3rd Floor>Unit 321

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#292: Complete cabinets, countertops, and trim

Type: Location:
3rd Floor>Unit 321

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

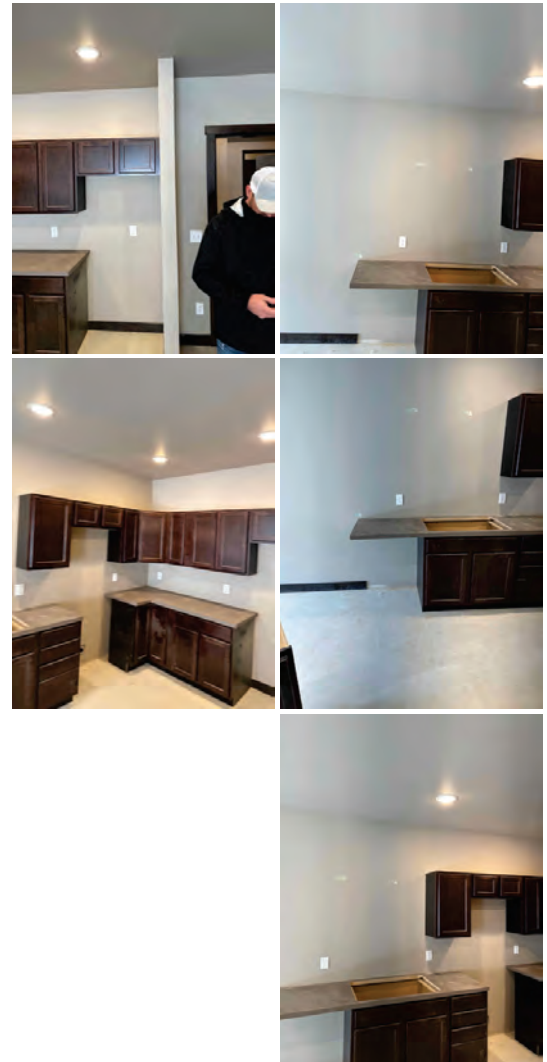

#293: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#294: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#295: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#296: Repair water damaged drywall at bedroom window

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#297: Seal AC can

Type:	Location: 3rd Floor>Unit 321
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#298: Complete flooring

Type:

Location:

3rd Floor>Unit 321

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#299: Drywall patch

Type:

Location:

3rd Floor>Unit 321



Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

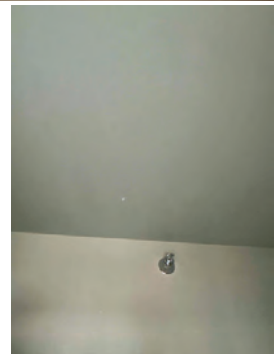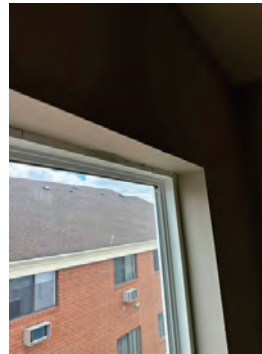Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#268: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#269: Shelving Missing

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#271: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#272: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#273: Complete flooring

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#274: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 323
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#275: Seal AC can

Type: Location:
3rd Floor>Unit 323

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#276: Repair water damaged drywall at bedroom window

Type: Location:
3rd Floor>Unit 323

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#277: Drywall patch

Type: Location:
3rd Floor>Unit 323

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated







Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

12 Items

#246: Deliver & Install appliances

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#247: Shelving Missing

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#248: Complete Mech/plumbing trim out

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#249: Repair water damaged drywall at living room window

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#250: Complete caulking at countertops & windows

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#251: Window latch inoperable living room

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#252: Seal AC can

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#253: Repair water damaged drywall at bedroom window

Type: Location:
3rd Floor>Unit 325

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

**#254: Complete cabinets, countertops, and trim**

Type: Location:
3rd Floor>Unit 325

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#255: Electrical incomplete**

Type: Location:
3rd Floor>Unit 325

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#256: Complete flooring

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#257: Drywall patch

Type:	Location: 3rd Floor>Unit 325
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated







Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

3 Items

#97: Drywall patch

Type:

Location:

4th Floor>Fitness Center

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated


Description:

Wall for trash chute does not meet 2-hour



#98: Complete cabinets, countertops, and trim

Type:	Location: 4th Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#99: Complete flooring

Type:	Location: 4th Floor>Fitness Center
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items


#218: Complete flooring

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#219: Fire Extinguisher Cabinet Missing - RO too high

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#220: Sprinkler Escutcheons Missing

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#221: Masonry infill at elevator frame - needs 2HR rating

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#222: Drywall patch

Type:

Location:

4th Floor Hallway

Date Created:

Due Date:

04/17/2024


04/20/2024

Priority:


Status:

Initiated



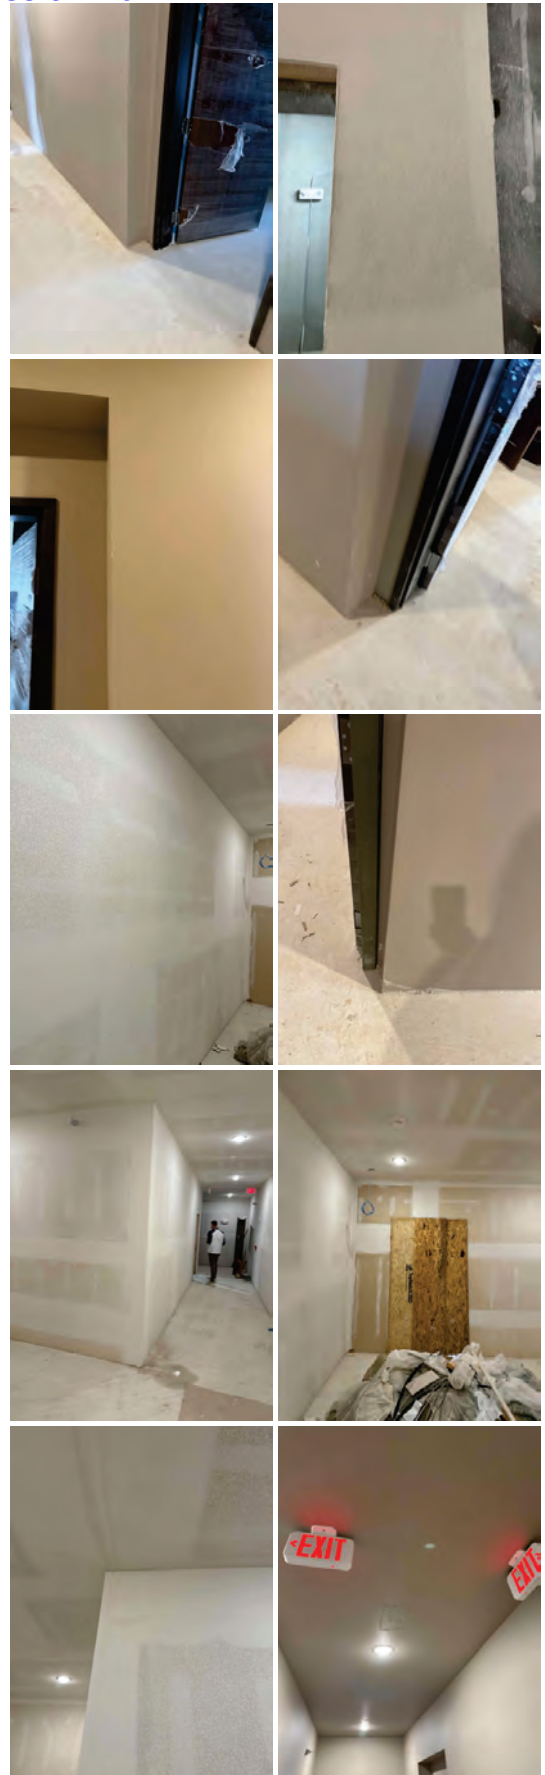



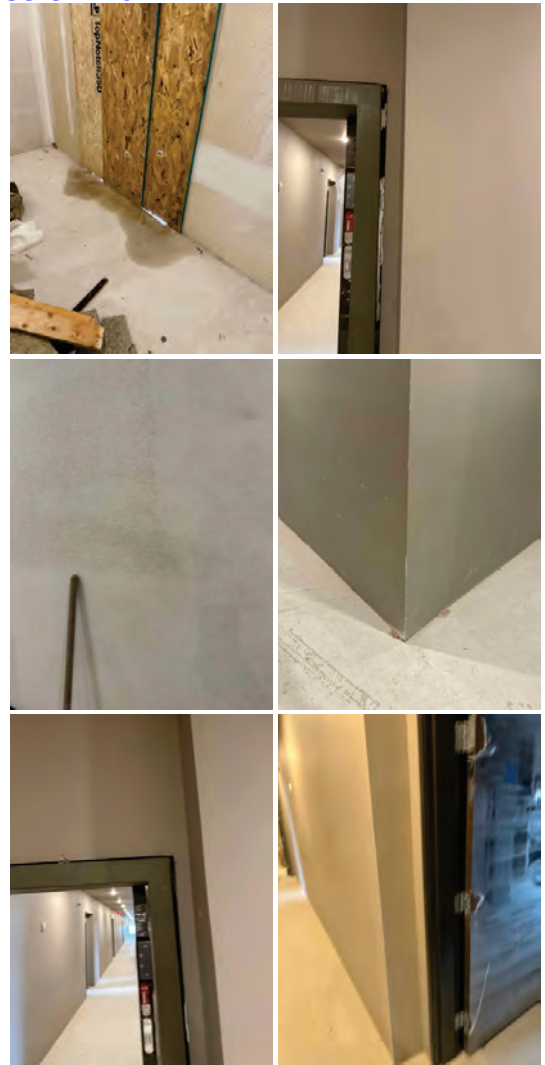

#223: Precast stairwell

Type:

Location:

4th Floor Hallway

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





#226: Electrical incomplete - empty boxes

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#240: Complete base

Type:	Location: 4th Floor Hallway
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations


7 Items

#100: Complete flooring

Type:	Location: 4th Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#101: Complete cabinets, countertops, and trim

Type:	Location: 4th Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#102: Electrical incomplete

Type: Location:
4th Floor>Mech/Jan't

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#103: Complete door hardware**

Type: Location:
4th Floor>Mech/Jan't

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

**#104: Fire stopping at penetrations**

Type: Location:
4th Floor>Mech/Jan't


Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#105: Sprinkler Escutcheons Missing

Type:	Location: 4th Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#106: Paint Door

Type:	Location: 4th Floor>Mech/Jan't
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704


Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

3 Items

#128: Complete door hardware

Type:	Location: 4th Floor>Storage
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#129: Complete flooring

Type:	Location: 4th Floor>Storage
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#130: Drywall patch

Type:

Location:

4th Floor>Storage

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

1 Items

#95: Drywall patch

Type:

Location:

4th Floor>Trash Chute

Date Created:

Due Date:

04/17/2024

04/20/2024


Priority:

Status:

Initiated

Description:

Wall does not meet 2-hour rating.





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

7 Items

#1: Install appliances

Type:	Location: 4th Floor>Unit 400
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#2: Complete flooring

Type:	Location: 4th Floor>Unit 400
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#3: Complete Mech/plumbing trim out

Type: Location:
4th Floor>Unit 400

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#4: Drywall patch

Type: Location:
4th Floor>Unit 400

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated


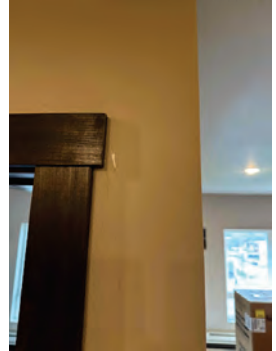




#5: Shelving Missing

Type: Location:
4th Floor>Unit 400

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#6: Complete door hardware

Type:	Location: 4th Floor>Unit 400
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#13: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 400
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#7: Shelving Missing

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#8: Complete cabinets and countertops

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#9: Install appliances

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#10: Complete flooring

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#11: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#12: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#15: Drywall patch

Type:	Location: 4th Floor>Unit 401
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



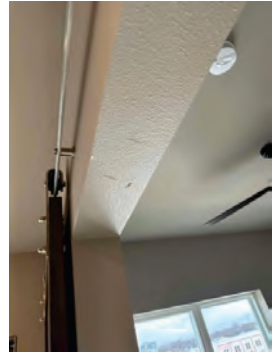

#16: Paint touch ups

Type:

Location:

4th Floor>Unit 401

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#25: Install appliances

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#26: Shelving Missing


Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#27: Electrical incomplete

Type: Location:
4th Floor>Unit 402

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

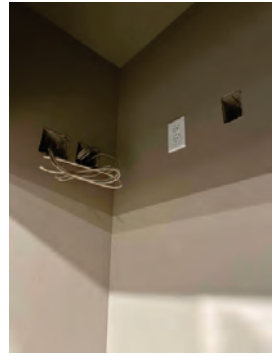


#28: Complete cabinets and countertops

Type: Location:
4th Floor>Unit 402

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



Description:
Not enough room for dishwasher

#29: Complete door hardware

Type: Location:
4th Floor>Unit 402

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#30: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#31: Complete flooring


Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#32: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#33: Complete bathroom mirror

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#34: Drywall patch

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#35: Window latch inoperable

Type:	Location: 4th Floor>Unit 402
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



Description:
Limiter disconnected and latches do not work in both bedrooms



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#17: Shelving Missing

Type:	Location: 4th Floor>Unit 403
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#18: Install appliances

Type:	Location: 4th Floor>Unit 403
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#19: Complete Mech/plumbing trim out

Type: Location:
4th Floor>Unit 403

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#20: Complete caulking at countertops & windows**

Type: Location:
4th Floor>Unit 403

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#21: Complete flooring

Type: Location:
4th Floor>Unit 403

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#22: Repair water damaged drywall at window

Type:	Location: 4th Floor>Unit 403
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:
Window leaking at head

#23: Complete door hardware

Type:	Location: 4th Floor>Unit 403
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

Spring hinges

#24: Complete bathroom mirror

Type:

Location:

4th Floor>Unit 403

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

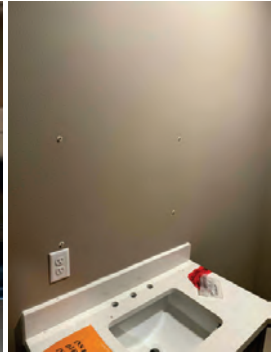



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#54: Install appliances

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#55: Shelving Missing

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#56: Complete door hardware

Type:

Location:

4th Floor>Unit 404

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#57: Electrical incomplete**

Type:

Location:

4th Floor>Unit 404

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#58: Window Pane Broken in living room**

Type:

Location:

4th Floor>Unit 404

Date Created:


Due Date:

04/17/2024**04/20/2024**

Priority:


Status:

Initiated



#59: Paint touch ups

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#60: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#61: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#62: Complete flooring

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#63: Window latch inoperable

Type:	Location: 4th Floor>Unit 404
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#65: Drywall patch

Type:

Location:

4th Floor>Unit 404

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#36: Install appliances

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#37: Shelving Missing

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:


#38: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:

#39: Repair water damaged drywall at living room window

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

Description:
Window leaking**#40: Complete flooring**

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#41: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#42: Repair water damaged drywall at bedroom window

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#43: Drywall patch

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#44: Electrical incomplete

Type:	Location: 4th Floor>Unit 405
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#76: Shelving Missing

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#77: Install appliances

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#78: Window Pane Broken in living room

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#79: Complete door hardware

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#80: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#81: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#82: Complete flooring

Type:	Location: 4th Floor>Unit 406
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#83: Drywall patch

Type: Location:
4th Floor>Unit 406

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#84: Electrical incomplete

Type: Location:
4th Floor>Unit 406

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#45: Install appliances

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#46: Finish paint & paint touch ups

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#47: Repair water damaged drywall at living room window

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#48: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#49: Complete flooring


Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#50: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#51: Window Pane Missing

Type:	Location: 4th Floor>Unit 407
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#52: Drywall patch

Type:

Location:

4th Floor>Unit 407

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





#53: Electrical incomplete

Type:

Location:

4th Floor>Unit 407

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#139: Shelving Missing

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#140: Install appliances

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#141: Electrical incomplete

Type:

Location:

4th Floor>Unit 408

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

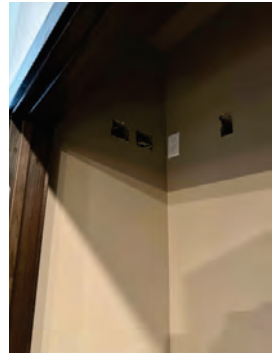

#142: Complete door hardware

Type:

Location:

4th Floor>Unit 408

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



#143: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#144: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#145: Complete flooring


Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#146: Window latch inoperable in bedroom

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#147: Paint touch ups

Type:	Location: 4th Floor>Unit 408
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#148: Drywall patch

Type:

Location:

4th Floor>Unit 408

Date Created:

Due Date:




04/17/2024

04/20/2024

Priority:

Status:

Initiated

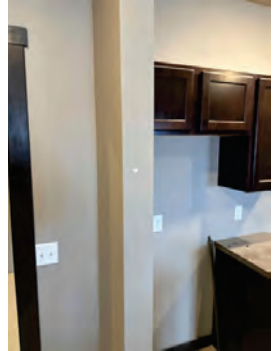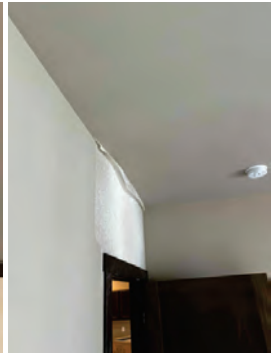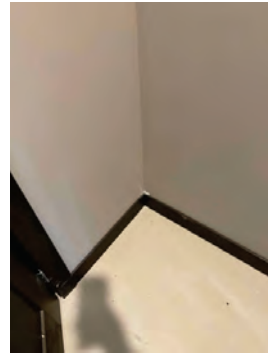



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#64: Shelving Missing

Type:	Location: 4th Floor>Unit 409
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#66: Install appliances


Type:	Location: 4th Floor>Unit 409
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#67: Paint touch ups

Type: Location:
4th Floor>Unit 409

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

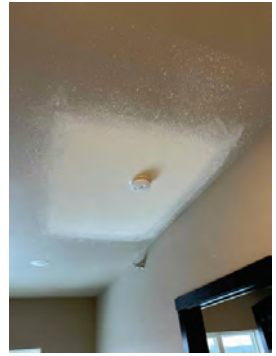

#68: Repair water damaged drywall at living room window

Type: Location:
4th Floor>Unit 409

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#69: Complete Mech/plumbing trim out

Type: Location:
4th Floor>Unit 409

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#70: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 409
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#71: Clean up paint

Type:	Location: 4th Floor>Unit 409
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#72: Complete flooring

Type:

Location:

4th Floor>Unit 409

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#73: Window latch inoperable in bedroom

Type:

Location:

4th Floor>Unit 409

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#74: Drywall patch

Type:

Location:

4th Floor>Unit 409


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

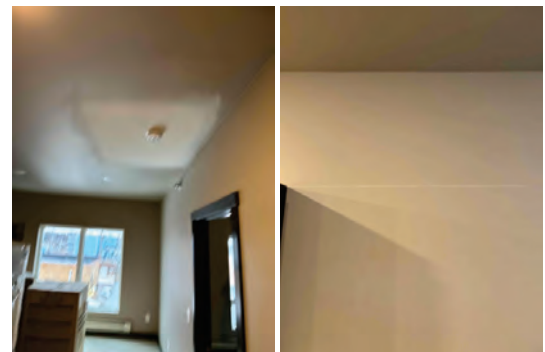Initiated



#75: Electrical incomplete

Type:

Location:

4th Floor>Unit 409

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#159: Install appliances

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#160: Shelving Missing

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#161: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#162: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#163: Complete flooring

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#164: Electrical incomplete

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#165: Window Pane Broken in bedroom

Type:	Location: 4th Floor>Unit 410
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#166: Drywall patch

Type:

Location:

4th Floor>Unit 410

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

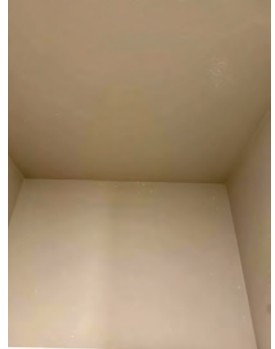



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#85: Install appliances


Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#86: Shelving Missing

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#87: Complete cabinets, countertops, and trim

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#88: Complete door hardware

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#89: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#90: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#91: Complete flooring

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#92: Electrical incomplete A-C: Gehrtz Construction Reports Page 345 of 410

Type:

Location:

4th Floor>Unit 411

Date Created:

04/17/2024


Due Date:

04/20/2024

Priority:

Status:

Initiated

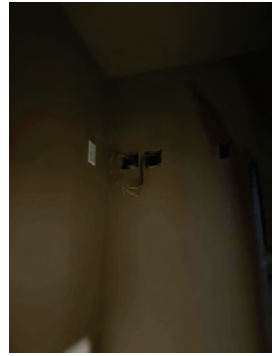

#93: Drywall patch

Type:

Location:

4th Floor>Unit 411

Date Created:

04/17/2024



Due Date:


04/20/2024

Priority:

Status:


Initiated






#94: Sprinkler Escutcheons Missing at bathroom

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#96: Permanent roof ladder/stair missing

Type:	Location: 4th Floor>Unit 411
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

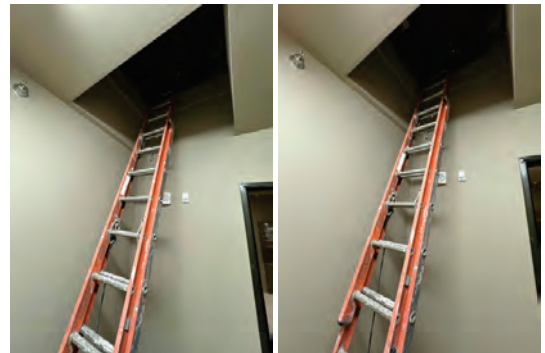



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

11 Items

#177: Install appliances

Type:	Location: 4th Floor>Unit 412
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#178: Shelving Missing

Type:	Location: 4th Floor>Unit 412
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#179: Complete bathroom mirror

Type: Location:
4th Floor>Unit 412

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

**#180: Complete cabinets, countertops, and trim**

Type: Location:
4th Floor>Unit 412

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#181: Complete caulking at countertops & windows**


Type: Location:
4th Floor>Unit 412

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#182: Window binding at living room - will not shut

Type:	Location: 4th Floor>Unit 412
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#183: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 412
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#184: Complete flooring

Type:

Location:

4th Floor>Unit 412

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#185: Drywall patch

Type:

Location:

4th Floor>Unit 412

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#186: Window latch inoperable in bedroom

Type:

Location:

4th Floor>Unit 412


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

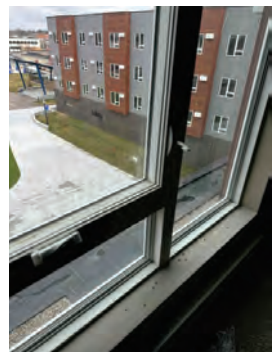Initiated

#187: Electrical incomplete

Type:

Location:

4th Floor>Unit 412

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

12 Items

#107: Install appliances

Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#108: Shelving Missing

Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#109: Paint touch ups

Type: Location:
4th Floor>Unit 413

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#110: Repair water damaged drywall at living room window

Type: Location:
4th Floor>Unit 413

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#111: Complete caulking at countertops & windows

Type: Location:
4th Floor>Unit 413

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#112: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#113: Complete flooring


Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#114: Electrical incomplete A-C: Gehrtz Construction Reports Page 355 of 410

Type: Location:
4th Floor>Unit 413

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

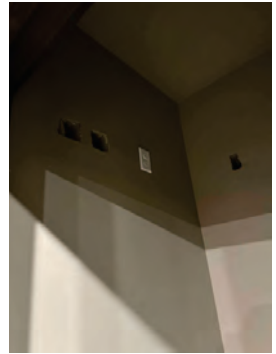

#115: Complete door hardware

Type: Location:
4th Floor>Unit 413

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





#116: Repair water damaged drywall at bedroom window

Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#117: Window latch inoperable in bedroom

Type:	Location: 4th Floor>Unit 413
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#118: Drywall patch

Type:

Location:

4th Floor>Unit 413

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#198: Install appliances

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#199: Shelving Missing


Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#200: Window latch inoperable in bedroom

Type: Location:
4th Floor>Unit 414

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



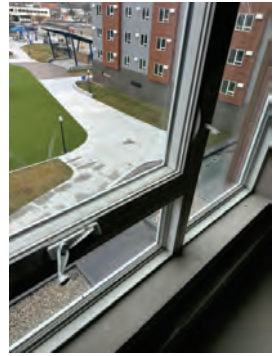


#201: Complete cabinets, countertops, and trim

Type: Location:
4th Floor>Unit 414

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#202: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#203: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#204: Complete flooring

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#205: Electrical incomplete

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#206: Drywall patch

Type:	Location: 4th Floor>Unit 414
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

9 Items

#119: Install appliances

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#120: Shelving Missing

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#121: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#122: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#123: Complete flooring

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated


#124: Window crank broken at living room

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#125: Electrical incomplete

Type:	Location: 4th Floor>Unit 415
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#126: Complete cabinets, countertops, and trim

Type:

Location:

4th Floor>Unit 415

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated**#127: Drywall patch**

Type:

Location:

4th Floor>Unit 415


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

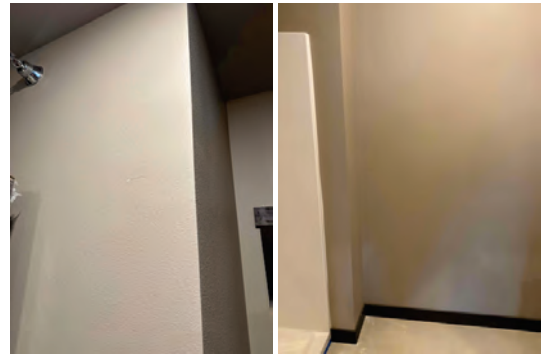Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

8 Items

#131: Shelving Missing

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#132: Install appliances

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#133: Complete caulking at countertops & windows


Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#134: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#135: Electrical incomplete

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#136: Complete flooring

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#137: Seal AC can

Type:	Location: 4th Floor>Unit 417
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#138: Drywall patch

Type:

Location:

4th Floor>Unit 417

Date Created:

Due Date:

04/17/2024

04/20/2024

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#149: Shelving Missing

Type:	Location: 4th Floor>Unit 419
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#150: Install appliances


Type:	Location: 4th Floor>Unit 419
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#151: Window latch inoperable in living room

Type: Location:
4th Floor>Unit 419

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#152: Paint touch ups

Type: Location:
4th Floor>Unit 419

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#153: Complete cabinets and countertops

Type: Location:
4th Floor>Unit 419

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#154: Complete caulking at countertops & windows

Type:	Location: 4th Floor>Unit 419
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#155: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 419
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#156: Complete flooring

Type:

Location:

4th Floor>Unit 419

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#157: Electrical incomplete

Type:

Location:

4th Floor>Unit 419

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#158: Drywall patch

Type:

Location:

4th Floor>Unit 419


Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

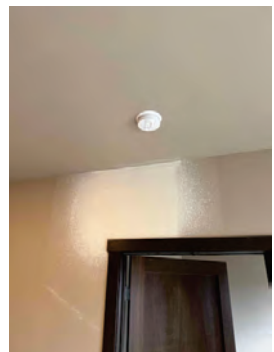Initiated



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#167: Shelving Missing

Type:	Location: 4th Floor>Unit 421
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#168: Install appliances

Type:	Location: 4th Floor>Unit 421
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#169: Repair water damaged drywall at window

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




Description:
Window leaking

#170: Paint touch ups

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

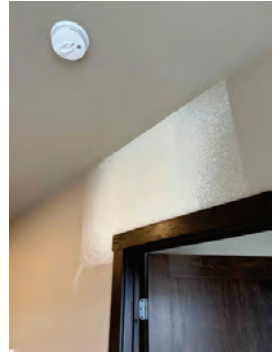

#171: Complete caulking at countertops & windows

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#172: Complete Mech/plumbing trim out

Type:	Location: 4th Floor>Unit 421
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#173: Complete flooring

Type:	Location: 4th Floor>Unit 421
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#174: Window Pane Broken in living room

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#175: Electrical incomplete**

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated


**#176: Drywall patch**

Type: Location:
4th Floor>Unit 421

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



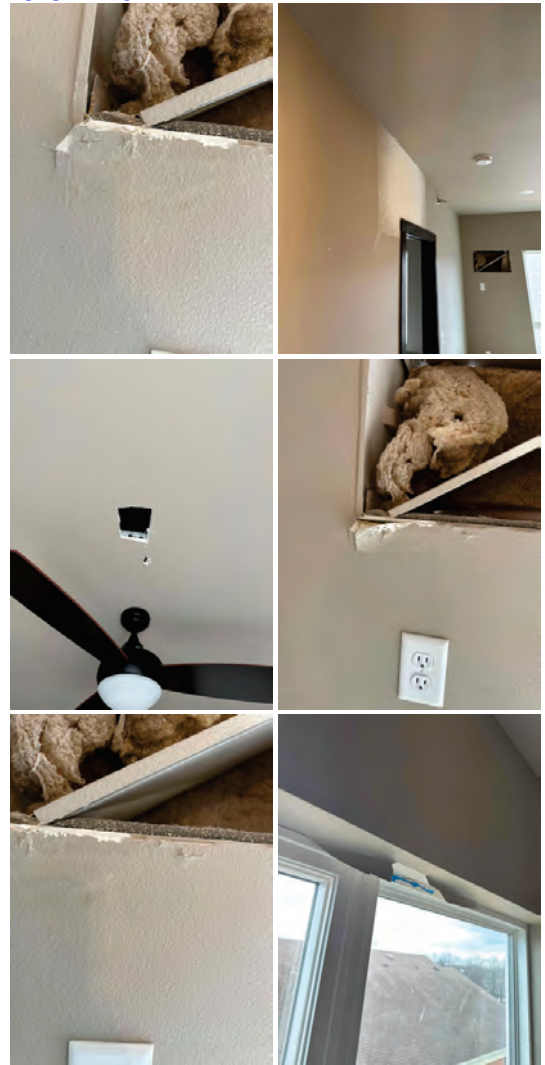



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

10 Items

#188: Install appliances

Type:	Location: 4th Floor>Unit 423
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#189: Shelving Missing


Type:	Location: 4th Floor>Unit 423
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#190: Window latch inoperable in living room

Type: Location:
4th Floor>Unit 423

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#191: Complete cabinets, countertops, and trim

Type: Location:
4th Floor>Unit 423

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#192: Complete caulking at countertops & windows

Type: Location:
4th Floor>Unit 423

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

#193: Complete Mech/plumbing trim out

Type:	Location:
	4th Floor>Unit 423
Date Created:	Due Date:
04/17/2024	04/20/2024
Priority:	Status:
	Initiated

#194: Repair water damaged drywall at window

Type:	Location:
	4th Floor>Unit 423
Date Created:	Due Date:
04/17/2024	04/20/2024
Priority:	Status:
	Initiated



#195: Complete flooring

Type:

Location:

4th Floor>Unit 423

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#196: Repair water damaged drywall at AC

Type:

Location:

4th Floor>Unit 423

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated

#197: Drywall patch

Type:

Location:

4th Floor>Unit 423

Date Created:

Due Date:

04/17/2024**04/20/2024**

Priority:

Status:

Initiated





Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations


11 Items

#207: Install appliances

Type:	Location: 4th Floor>Unit 425
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#208: Shelving Missing

Type:	Location: 4th Floor>Unit 425
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#209: Window latch inoperable in living room

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#210: Complete caulking at countertops & windows

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#211: Complete Mech/plumbing trim out

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

#212: Complete flooring

Type:	Location: 4th Floor>Unit 425
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#213: Repair water damaged drywall at living room window

Type:	Location: 4th Floor>Unit 425
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#214: Electrical incomplete

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated

**#215: Repair water damaged drywall at bedroom window**

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024


Priority: Status:
Initiated

**#216: Drywall patch**

Type: Location:
4th Floor>Unit 425

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated



#217: Complete cabinets, countertops, and trim

Type:

Location:

4th Floor>Unit 425

Date Created:

Due Date:


04/17/2024

04/20/2024

Priority:

Status:

Initiated

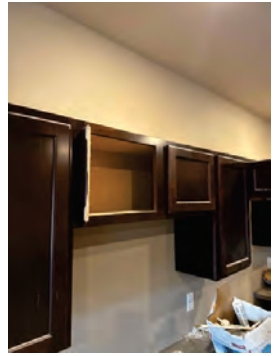



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations

2 Items

#224: ALL Vent pipes are still capped at roof

Type:

Location:

Roof

Date Created:

04/17/2024

Due Date:

04/20/2024

Priority:

Status:

Initiated



#225: Roof items

Type:

Location:

Roof

Date Created:

04/17/2024

Due Date:



04/20/2024





Priority:



Status:




Initiated




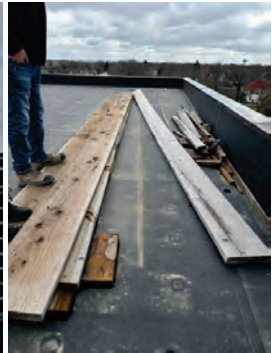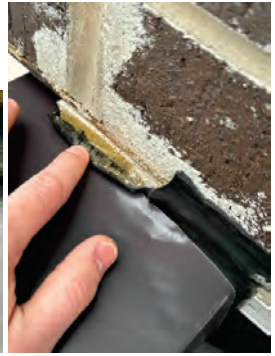

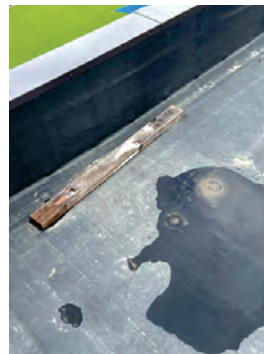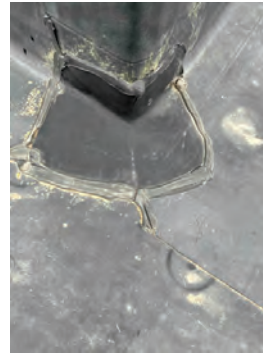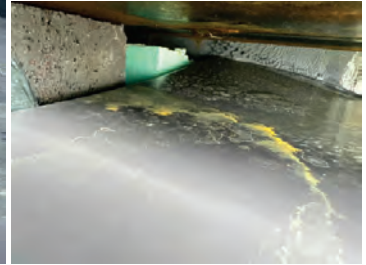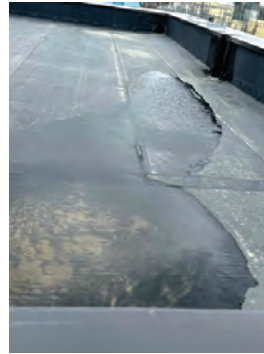

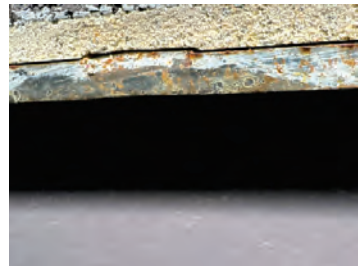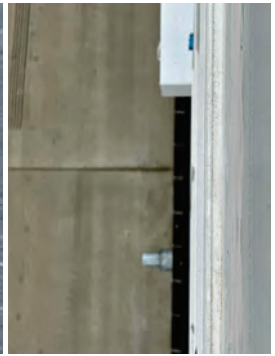

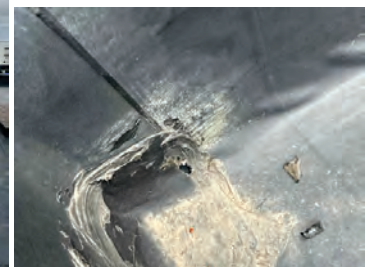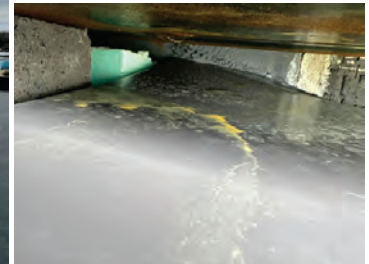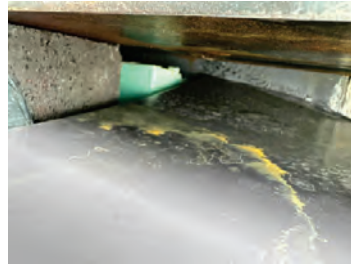

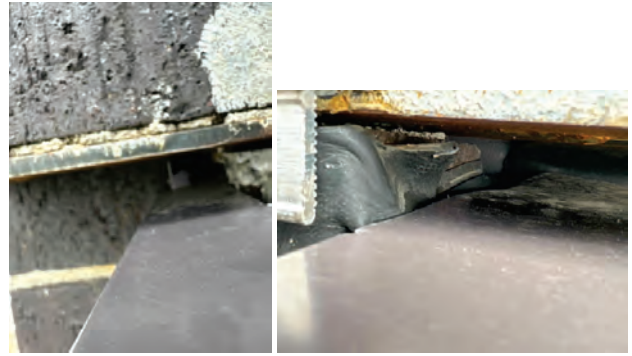



Gehrtz Construction Services
510 4th Ave. N
Fargo, North Dakota 58102
United States
(701) 297-0704

Job #: 24-020 The Ruins Observations
315 Kemp Ave E
Watertown South Dakota.

Punch Items for 24-020 - The Ruins Observations


9 Items


#227: Complete flooring

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated

#228: Fire caulk joints and penetrations

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated





#229: Remove board

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#230: Finish top cap

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#231: Remove adhesive

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated




#232: Complete grout at precast panels

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status:



#233: Paint walls

Type:	Location: West Stairwell
Date Created: 04/17/2024	Due Date: 04/20/2024
Priority:	Status: Initiated



#234: Complete door hardware

Type: Location:
West Stairwell

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated




#235: Railing missing at center stairwell wal

Type: Location:
West Stairwell

Date Created: Due Date:
04/17/2024 04/20/2024

Priority: Status:
Initiated





September 27th, 2024

Charles Aarestad
Executive Vice President
Red River State Bank
300 2nd Ave West
Halstad, MN 56548

Re: The Ruins Mixed-use Development
Watertown, SD

Project No. 24-020

Dear Mr. Aarestad:

Gehrtz Construction Services (GCS) is pleased to present our independent third-party follow up inspection and report for The Ruins. We understand the subject is an under construction 63-unit mid/high rise property at 315 East Kemp Ave in Watertown, SD. Upon completion, the property will consist of a single, four-story apartment building with on-grade parking and first floor retail/ commercial space occupied by the City of Watertown.

A full and detailed inspection was created documenting observations made on site April 17th, 2024. GCS personnel arrived on site September 24th at 12:30 pm to perform a follow up inspection. The inspection was completed at 2 pm.

GCS observed no significant advancement in work on the project since the first site inspection on April 17th, 2024. Please reference the previous site inspection report for all details pertaining to work remaining. In addition, areas that were noted showing signs of water penetration and damage in the previous report appeared to have deteriorated further from the time of original inspection on April 17th, 2024. The following page contains photos showing this deterioration.

Thank you for the opportunity, please do not hesitate to reach out with any questions.

Sincerely,

A handwritten signature in black ink, appearing to read "Matt Gehrtz". The signature is stylized with a long, horizontal flourish extending to the right.

Matt Gehrtz




4th Floor Unit,
April 17, 2024



4th Floor Unit,
Sept. 24, 2024



4th Floor Unit,
Sept. 24, 2024

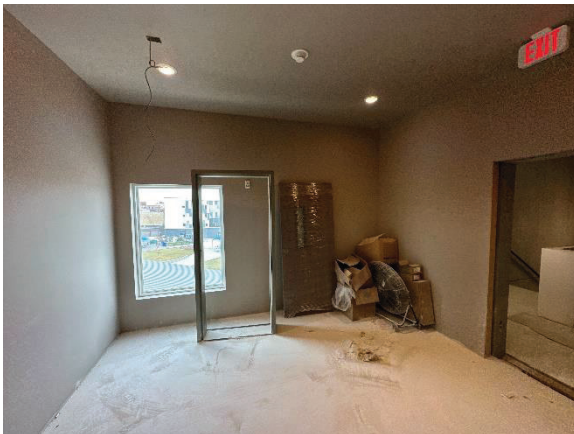


4th Floor Hall,
April 17, 2024




4th Floor Hall,
Sept. 24, 2024



4th Floor Unit,
April 17, 2024

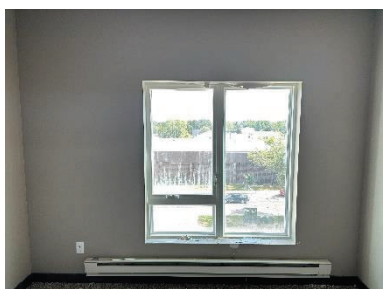


4th Floor Unit,
Sept. 24, 2024

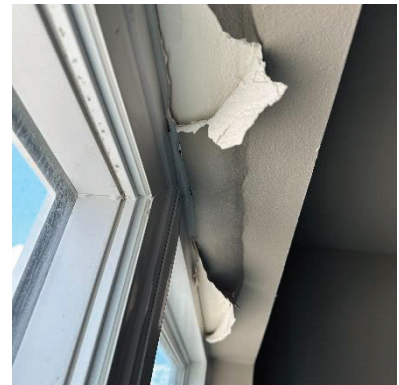


4th Floor Unit,
Sept. 24, 2024



4th Floor Unit,
April 17, 2024

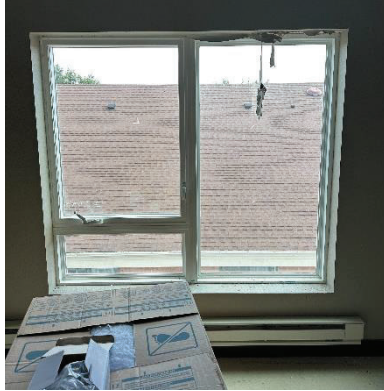

4th Floor Unit,
Sept. 24, 2024

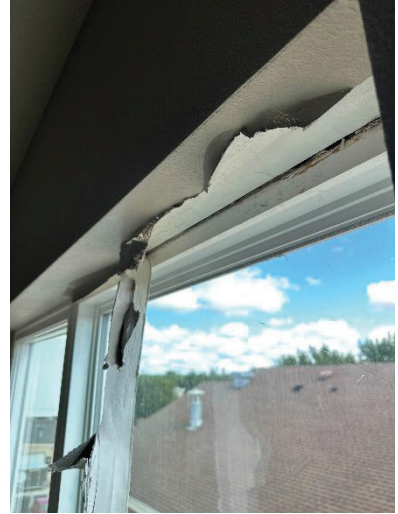

4th Floor Unit,
Sept. 24, 2024



4th Floor Unit,
April 17, 2024



4th Floor Unit,
Sept. 24, 2024



4th Floor Unit,
Sept. 24, 2024



June 10th, 2025

Charles Aarestad
Executive Vice President
Red River State Bank
300 2nd Ave West
Halstad, MN 56548

Re: The Ruins Mixed-use Development
Watertown, SD

Project No. 24-020

Dear Mr. Aarestad:

Gehrtz Construction Services (GCS) is pleased to present our independent third-party follow-up inspection and report for our Opinion of Cost to Complete for The Ruins. We understand the subject is an under construction 63-unit mid/high rise property at 315 East Kemp Ave in Watertown, SD. Upon completion, the property will consist of a single, four-story apartment building with on-grade parking and first floor retail/ commercial space occupied by the City of Watertown.

A full and detailed inspection was created documenting observations made on site April 17th, 2024. GCS personnel completed a follow-up inspection on September 24th, 2024. GCS personnel completed a second follow-up inspection on May 6th, 2025 to prepare an Opinion of Cost to Complete report.

GCS observed no significant advancement in work on the project since the previous site inspection on September 24th, 2024. At the time of the inspection, work to repair the drywall damage caused by moisture penetration appeared to be ongoing. However, additional moisture damage was observed at the heads and sills of the windows of areas that were actively being repaired. Since ongoing moisture penetration was observed, GCS engaged Service Master to provide an estimate based on their professional opinion of the cost to test, mitigate and repair any effects of moisture penetration. The Opinion of Cost to Complete as well as the estimate for Water & Mold Mitigation Report are attached for your consideration.

Thank you for the opportunity, please do not hesitate to reach out with any questions.

Sincerely,

A handwritten signature in black ink, appearing to read "Matt Gehrtz".

Matt Gehrtz



Red River State Bank - The Ruins

Opinion of Cost to Complete

Watertown, SD

May 13, 2025

Project 24-020

BID PACKAGE	OPINION OF COST TO COMPLETE	ASSUMED SCOPE OF WORK TO COMPLETE
General Conditions	\$ 50,000.00	
Testing & Inspections	\$ 39,555.00	Triple \$5m Watertown permit fee
Foundation removal	\$ -	
Site Survey/Civil	\$ -	
Soil Borings	\$ -	
Building Demolition	\$ -	
Concrete	\$ 27,000.00	Re-work garage entry
Asbestos	\$ -	
Concrete - Waterproofing & Insulation	\$ -	
Excavation	\$ -	
Precast Concrete - Materials / Erection	\$ -	
Gypcrete	\$ -	
CMU Block	\$ 50,000.00	1,000sf, assumptions on 1st floor
Move Utilities	\$ -	
Misc. Metals	\$ 60,000.00	300 lf of railin on 2nd roof
General W&L Rough Carpentry Labor	\$ 10,000.00	Allowance of 80 hrs
General W&L Rough Carpentry Materials	\$ -	
General W&L Finish Carpentry Labor	\$ 12,500.00	Install 3 units of cabinets, install frames in commercial spaces
General W&L Finish Carpentry Materials	\$ -	Assuming all materials on site
Millwork - Cabinets	\$ 9,000.00	assuming 3 units of cabinets need to be replaced
Countertops - Kitchen & Bathroom	\$ 6,000.00	assuming 3 units worth of ct needs to be replaced
Bathroom Vanities	\$ -	
Wood Components / Trusses	\$ -	
Moisture Protections	\$ 80,000.00	2000sf pavers
Building Insulation	\$ -	
Masonry	\$ 90,000.00	2,500sf and mobilization
Metal Siding / Metal Panels	\$ 195,000.00	new tyvek, install panels and new tyvek over existing tyvek (13,00)
Sealants	\$ 182,712.00	Complete package
Commercial Doors, Frames & Hardware	\$ 2,500.00	Assuming all materials on site
Residential Wood Doors & Frames	\$ -	
Overhead Doors	\$ 10,000.00	New door for alley entrance
Vinyl Windows	\$ 3,000.00	5 window replacement, misc. window removable stop repair
Glass & Glazing	\$ -	
Drywall	\$ 5,250.00	Lobby walls on 1st
Carpet (Materials)	\$ 120,000.00	Assuming no material on site, 2/3 LVT and 1/3 broadloom carpet
Carpet (Install)	\$ 50,000.00	Install 2/3 LVT and 1/3 broadloom
Painting / Staining	\$ 51,000.00	Common area painting with 15k allowance for touch ups
Fill Nail Holes	\$ -	
Postal Specialties/Bike Rack/Door Markers	\$ 8,700.00	supply postal boxes
Exterior Signage	\$ 30,000.00	Supply install new large building sign
Fire Extinguishers & Cabinets	\$ 1,000.00	Install cabinets throughout, assuming all are on site.
Ceiling Fans	\$ -	
Closet Shelving	\$ 25,000.00	Supply and install 63 units of wire shelving
Toilets/Accessories	\$ 30,000.00	Supply/install toilet partitions, accessories on 1st
Appliances & AC Units	\$ 160,000.00	Supply 42 units, install 63 units
Kitchen Sinks/Faucets	\$ -	
Bath Faucets/Shower Heads	\$ -	
Bathroom Mirrors	\$ -	
Window Treatments	\$ 30,000.00	Supply 147 blinds
Conveying Systems	\$ 90,000.00	complete elevator and testing
Building Sprinkler	\$ 15,000.00	fill system, commercial space trim out and minor piping
Plumbing	\$ 100,000.00	63 unit trim out, complete w/v in garage, 2 commercial bathroom trim out
HVAC	\$ 25,000.00	Trim out Unit bathrooms, Finish 1st Floor
Electrical/Security System	\$ 125,000.00	Per Fusion
Accrued Interest	\$ -	
Paving & Sidewalks	\$ 2,750.00	1200 lf striping, 1 hc stall
Site Fencing / Accessories / Dumpster Enclosure	\$ -	No location shown in plans
Total Bid Packages	\$ 1,695,967.00	

Exclusions:

Does not factor any cost associated with water damage mediation and remedies
Does not include current liens on building as of May, 2025

Assumptions:

Most materials on site, U.N.O.
extents of 1st floor lobby/bathroom work was assumed based on old plans
all wire pulled, power live into the building
all mechanical and plumbing fixtures for floors 2-4 are on site



SCOPE OF WORK

servicemasterrestore.com/commercial

SCOPE OF WORK: "THE RUINS"

Service Address:

Project: Water & Mold Mitigation – The Ruins Apartments

Location: 315 Kemp Ave E, Watertown, SD

Client: United

Prepared By: Derek Moline – ServiceMaster by Moline

Date: June 6th 2025

Submitted to:

Name: Matt Gehrtz – Gehrtz Construction

Email: mgehrtz@gcs-fm.com

Phone: 701-367-3342

Submitted By:

Name: Derek & Steve Moline

Email: dmoline@servicemaster-pro.com

Phone: 701-640-7430 (cell)

INTRODUCTION

Thank you for the opportunity to prepare a detailed restoration plan for your facility. We look forward to working with you and your team as we utilize our specialized restoration resources to limit interruption to your business during the recovery process.

Your business is our business, so rest assured that our team is your team, and we understand the situation at hand. With this in mind, it is our plan to restore your facility, under your direction, as quickly and efficiently as possible, employing industry "Best Practices" and procedures.

Please, do not hesitate to call us with any questions or thoughts you may have regarding the recovery process. Thank you once again, we look forward to working with you and your team.

Respectfully submitted,
Derek & Steve Moline
Owners



SCOPE OF WORK

servicemasterrestore.com/commercial

Project Overview

This scope of work outlines the remediation and drying services required on the **north and east sides** of *The Ruins* apartment complex due to water intrusion and potential microbial growth. The objective is to mitigate water damage, prevent mold spread, and restore affected areas to a safe and stable condition.

Areas Affected

Work will be performed in the following units and common areas:

- **2nd Floor Units:** 201, 203, 205, 207, 209, 211, 213, 215, 217, 219, 221, 223, 225
- **3rd Floor Units:** 303, 305, 307, 309, 311, 313, 315, 317, 319, 321, 323, 325, 310
- **4th Floor Units:** 401, 403, 405, 407, 409, 411, 413, 415, 417, 419, 421, 423, 425
- **Common Areas:** 2nd Floor Hallway, 3rd Floor Hallway, 4th Floor Hallway

Scope of Work

1. **Containment & Safety Measures**
 - Install containment barriers and implement negative air pressure to prevent cross-contamination.
 - Clearly mark work zones with appropriate signage.
 - Ensure compliance with safety and IICRC standards.
2. **Selective Demolition**
 - Remove affected drywall and insulation on north and east sides of listed units and hallways.
 - Demolition to include only materials verified by moisture readings or visual damage.
3. **Moisture Mapping & Monitoring**
 - Conduct comprehensive moisture inspections of all identified areas.
 - Deploy drying equipment (air movers and dehumidifiers) to achieve dry standard per IICRC guidelines.



SCOPE OF WORK

servicemasterrestore.com/commercial

- Maintain daily moisture logs.
- 4. **Microbial Remediation (If Required)**
 - Apply antimicrobial treatment to exposed surfaces.
 - Remove and properly dispose of mold-contaminated materials under containment protocol.
 - Perform HEPA vacuuming and detailed cleaning per IICRC S520 standards.
- 5. **Drying & Filtration Equipment**
 - Utilize HEPA air scrubbers, dehumidifiers, and air movers throughout the drying phase.
 - Equipment will be monitored daily and adjusted as necessary.
- 6. **Documentation & Reporting**
 - Provide photo documentation before, during, and after work.
 - Maintain detailed job logs, drying logs, and equipment tracking.
 - Final reporting to include verification of dry standard or post-remediation clearance.

Rough Order of Magnitude (ROM) Estimate

Total Estimate: \$293,951.43

This ROM includes labor, equipment, materials, and disposal associated with the outlined mitigation work. Final cost may vary based on actual findings and required scope.

Exclusions

- Reconstruction/build-back services
 - Environmental lab testing or air clearance unless separately contracted
 - Asbestos or lead abatement
 - Contents manipulation or pack-out services unless specified
-

Estimated Project Duration

Estimated timeline: 22 days, pending site conditions and access.



SCOPE OF WORK

servicemasterrestore.com/commercial
